



November 29, 2011

Mr. Todd Del Frate  
California Regional Water Quality Control Board  
Central Valley Region  
11020 Sun Center Drive #200  
Rancho Cordova, CA 95670

**Re: Completion Report for Bin Storage Area/Metal Yard Regrading Project - August 12, 2011 Notice of Violation, Yuba-Sutter Disposal Inc. Landfill (Recology Yuba-Sutter Landfill), Yuba County**

Dear Mr. Del Frate,

This letter provides a report of project completion for the regrading of our Bin Storage Area/Metal Yard which is located on a portion of the closed Yuba-Sutter Disposal Inc. (YSDI) Landfill. The purpose of the project, as described in our September 14, 2011 Workplan, was to promote surface water drainage and eliminate an area of ponding described in your August 12, 2011 Notice of Violation. Although the NOV originally specified a completion date of October 31, 2011, we requested, and you granted by email, an extension to November 15, 2011, with report due by December 1.

For this project, Recology Yuba-Sutter (RYS) imported approximately 725 tons of material, including 300 tons of crushed recycled concrete and 225 tons of screened dirt to fill low spots and re-establish positive drainage in the south/southeast area of the yard. Our contractor imported and used an additional 155 tons of Class 2 aggregate to construct a perimeter berm of approximately 1,050 linear feet on the south and east perimeter of the Bin Storage Area/Metal Yard. This berm directs storm water runoff to an existing storm water discharge point, StW-1, located in the northeast corner of the yard. Our contractor also installed rock berms perpendicular to the perimeter drainage swale to reduce storm water velocity using 42 tons of five-inch washed angular green rock.

A record drawing documenting the final grades prepared by MHM Engineers and dated November 11, 2011 is attached. Four photos showing the area of the completed project are also attached.

If you have questions or need additional information about this specific project or post-closure maintenance activities in general, please contact either Bryan Clarkson at 707-693-2108 or me at 530-743-6933.

Sincerely,



Maggie Johnson  
Environmental Compliance and Safety Manager

Attachments (2)

- cc: Stephanie Kendall, Yuba County Environmental Health
- Bryan Clarkson, Recology Environmental Solutions
- Amy Dietz, Recology Corporate



PROJECT	RECORD DRAWING
DATE	11/01/11
SCALE	AS SHOWN
DESIGNED BY	WALTER
CHECKED BY	
APPROVED BY	

DATE	08/20/11
DESIGNED BY	WALTER
CHECKED BY	
APPROVED BY	
PROJECT	RECORD DRAWING
DATE	11/01/11
SCALE	AS SHOWN
DESIGNED BY	WALTER
CHECKED BY	
APPROVED BY	

Job Title  
**RECOLOGY YUBA-SUTTER  
 METAL YARD DRAINAGE  
 IMPROVEMENTS**

Sheet  
 reference  
 number:  
 Sheet 1 of 1


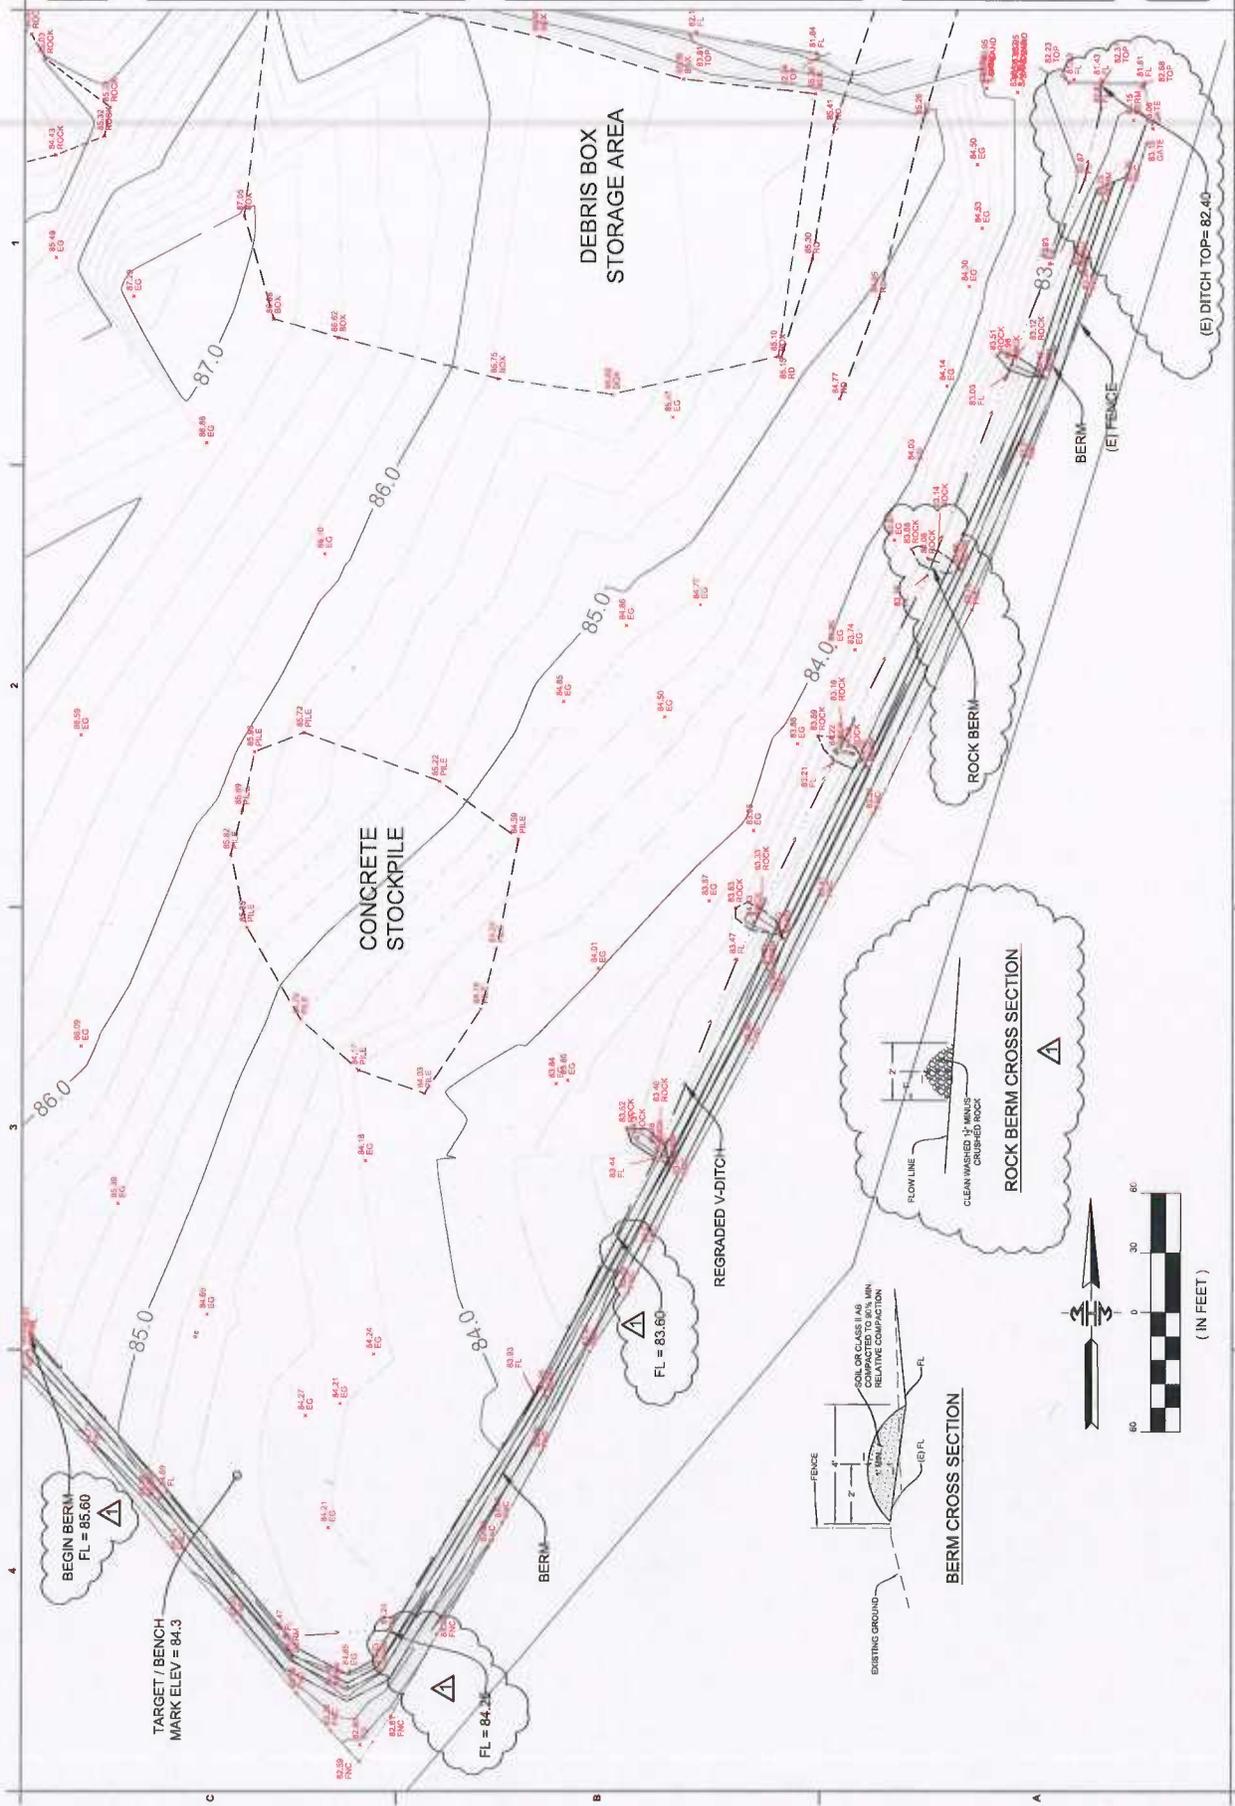






Photo 1: V-ditch drainage swale and berm looking east towards Yuba River



Photo 2: South perimeter fence line, V-ditch drainage swale, and berm



Photo 3: Southern end of Debris Box Storage/Metal Yard filled and regraded



Photo 4: V-Ditch drainage swale with perpendicular rock berms for storm water velocity control
