

**Monitoring Report Submittal Transmittal Form**

Attn: Guy Childs (916) 464-4648  
Central Valley Regional Water Quality Control Board  
11020 Sun Center Drive #200  
Rancho Cordova, CA 95670-6114

Discharger: The Morning Star Packing Company, LP and Fred Gobel  
Name of Facility: Williams Facility  
WDRs Order Number: R5-2013-0144  
WDID: 5A062005001  
County: Colusa

I am hereby submitting to the Central Valley Water Board the following information:

**Check all that apply:**

Monthly Monitoring Report for the month of APRIL 2015  
1st / 2nd / 3rd / 4th (circle one) Quarterly Monitoring Report for the year of N/A  
1st / 2nd (circle one) Semi-annual Monitoring Report for the year N/A  
Annual Monitoring Report for the year N/A

**Violation Notification**

During the monitoring period, there were / were not (circle one) any violations of the WDRs.

- The violations were: (add extra pages as needed) SETTLING POND WAS DRAINED BY 11/1/14, HOWEVER, ACCUMULATED SLUDGE AND SEDIMENT CANNOT BE REMOVED UNTIL MAY/JUNE 2015.
- Have the violations been corrected? Yes / No. If no, what will be done to correct the violations: (add extra pages as needed) THE SETTLING POND WILL BE EXCAVATED AND APPLIED TO LAA IN MAY/JUNE 2015

**Certification Statement**

"I certify under penalty of law that I have personally examined and am familiar with the information submitted in this document and all attachments and that, based on my inquiry of those individuals immediately responsible for obtaining the information, I believe that the information is true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment."

Signature: [Signature] Phone: (530)666-6600  
Printed Name: ROSS OLIVEIRA Date: 5/27/15



# THE MORNING STAR PACKING COMPANY

724 Main Street, Woodland CA 95695

22 May 2015

Mr. Guy Childs  
Central Valley Regional Water Quality Control Board  
11020 Sun Center Drive #200  
Rancho Cordova, CA 95670-6114

Re: Monthly Report for The Morning Star Packing Company – Williams, according to Waste Discharge Requirements Order No. R5-2013-0144.

Dear Mr. Childs:

Please find herewith the April Report with items requested in the Monthly Monitoring Reports section of the Monitoring and Reporting Program No. R5-2013-0144.

*1. Tabulated pond monitoring data.*

There are no tabulated cooling pond monitoring results for April as the pond was dry, however, a April logsheet is included as **Attachment A**.

*2. Tabulated daily flow measurements from each wastewater source and supplemental irrigation water to each check in each LAA field.*

As The Morning Star Packing Company – Williams is not processing, there are no daily flow measurements from the washwater sources. The April logsheet is included as **Attachment B**.

*3. The cumulative annual wastewater (Station 1 and Station 2) flow discharged to the LAAs to date, the average daily flow for the month, and comparison to the average daily flow limit.*

As The Morning Star Packing Company – Williams is not processing the April average daily flow is zero and a comparison to the average daily flow limit is not needed. The cumulative annual washwater from Station 1 and Station 2 are provided below and included in **Attachment B**:

Source	Annual Flow	Flow Limit
Station 1: Settling Pond/Gutters	0	
Station 2: Cooling Pond	0	
Total Washwater Discharge	0	422,000,000

Williams  
2211 Old HWY 99  
Williams, California  
95987

Santa Nella  
12045 S Ingomar Grade Rd  
Los Banos, California  
93635

Los Banos  
13448 Volta Rd  
Los Banos, California  
93635



4. *Tabulated wastewater monitoring data and calculation of the running average for each group of three consecutive sample results for BOD and total nitrogen.*

As The Morning Star Packing Company – Williams is not processing, there is no wastewater monitoring data and calculations to be submitted, however, a April logsheet is included as **Attachment C**.

5. *A current site plan depicting the irrigation checks within each LAA field that will be used during the calendar year, including all water conveyance ditches and internal berms that divide each LAA (where applicable).*

An updated 2014 site plan for the facility's LAA and individual field maps are provided in **Attachment D**.

6. *Tabulated update cropping information for each LAA field that includes at least:*

- a. *The crop that will be grown in each field;*
- b. *Planned and actual planting dates;*
- c. *Planned and actual harvest dates;*
- d. *Planned and actual cattle grazing schedule, location of cattle grazing, including the number of head on each field;*
- e. *Typical maximum expected and actual yield at harvest in applicable crop units per acre;*
- f. *Crop total nitrogen demand; and*
- g. *Crop average evapotranspiration rate in inches*

The tabulated cropping information for each LAA is included as **Attachment E**.

7. *Tabulated land application area monitoring data for each LAA field, including; calculation of the hydraulic loading, irrigation cycle average BOD loading, and total nitrogen loading to date from all sources. The average of the three most recent monitoring results shall be used to determine irrigation cycle average BOD and total nitrogen loading. Loading rates for Settling Pond solids, residual solids, cattle manure and commercial fertilizers shall be calculated separately using actual load analytical results and application areas.*

The tabulated land application area monitoring data for each LAA field are also included as **Attachment E**.

8. *A summary of the daily pre-application inspection reports for the month.*

As The Morning Star Packing Company – Williams is not processing, there is no pre-application inspection reports to submit, however, a April logsheet is included as **Attachment F**.

9. Calculation of the flow-weighted average FDS concentration to date (representative of the Settling Pond and plant sanitation/clean-up water) as monitored at Station 1.

As The Morning Star Packing Company – Williams is not processing, there is no calculation of the flow-weighted average FDS concentration to report, however, this information is presented at the bottom of **Attachment C**.

10. Residual solids monitoring data and monthly mass of residual solids generated and applied to each LAA field and/or disposed of off-site.

As The Morning Star Packing Company – Williams is not processing, there is no residual solids monitoring data to report, however, a April logsheet is included as **Attachment G**.

11. A comparison of monitoring data to the flow limitations, effluent limitations; mass loading limitations (for each LAA field), and discharge specifications, and an explanation of any violation of those requirements.

As The Morning Star Packing Company – Williams is not processing, there is no comparison of monitoring data to the flow limitations, effluent limitations, mass loading limitations or discharge specifications.

12. If requested by staff, copies of laboratory analytical report(s).


As The Morning Star Packing Company – Williams is not processing, there are no laboratory analytical reports to be submitted.

13. Copies of current calibration logs for all field test instruments.

The calibration log for April is included as **Attachment H**.

*"I certify under penalty of law that this document and all attachments have been prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. The information submitted is, to the best of my knowledge and belief, true, accurate and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment."*

Respectfully yours,

  
Ross Oliveira

# **Attachment A**

**MONTHLY MONITORING REPORT**

MONTH 

April
-------

  
 YEAR 

2015
------

DISCHARGER: Morning Star Packing Company, LP and Fred Gobel  
 FACILITY: Morning Star Tomato Packing Plant  
 COUNTY: Colusa  
 WDRs Order: R5-2013-0144

**POND MONITORING RESULTS: No water in pond**

Monitoring Location	Monitoring Week	Monitoring Date	Monitoring Time	Dissolved Oxygen <sup>1</sup> (mg/L)	pH	Freeboard (0.1 feet)	Odors <sup>3</sup>	Monthly Pond Berm/Leeve Condition <sup>4</sup>	Technican's Initials
Settling Pond	Week 1								
	Week 2								
	Week 3								
	Week 4								
	Week 5								
Coolng Pond	Week 1								
	Week 2								
	Week 3								
	Week 4								
	Week 5								

Sample frequency shall be weekly during the processing season and monthly during the non-processing season.

<sup>1</sup>Samples shall be collected at a depth of one foot from each pond in use, opposite the inlet.

<sup>2</sup>Freeboard shall be measured to the nearest 0.1 foot from staff gauge.

<sup>3</sup>Odors shall be reported as (none, slight, moderate, strong)

<sup>4</sup>If a pond berm/leeve conditon is not reported as good, a description of the condition of the berm/leeve shall be provided, as well as the maintenance that was completed.

# **Attachment B**

MONTHLY MONITORING REPORT

DISCHARGER: Morning Star Packing Company, LP and Fred Gobel  
 FACILITY: Morning Star Tomato Packing Plant  
 COUNTY: Colusa  
 WDRs Order: R5-2013-0144

MONTH   
 YEAR

FLOW MONITORING RESULTS :

Monitoring Date (Day of Month)	Flow Source					
	Supplemental GCID-Irrigation Water (gallons; calculated)	Station 1 - Settling Pond Water (gallons; meter)	Station 2 - Cooling Pond Water (gallons; meter)	Station 3 - Total Discharge to LAAs (gallons; meter)	Names of LAAs Irrigated	Station 3 - Total Discharge to LAAs (inches)
1	0	0	0	0	-	0
2	0	0	0	0	-	0
3	0	0	0	0	-	0
4	0	0	0	0	-	0
5	0	0	0	0	-	0
6	0	0	0	0	-	0
7	0	0	0	0	-	0
8	0	0	0	0	-	0
9	0	0	0	0	-	0
10	0	0	0	0	-	0
11	0	0	0	0	-	0
12	0	0	0	0	-	0
13	0	0	0	0	-	0
14	0	0	0	0	-	0
15	0	0	0	0	-	0
16	0	0	0	0	-	0
17	0	0	0	0	-	0
18	0	0	0	0	-	0
19	0	0	0	0	-	0
20	0	0	0	0	-	0
21	0	0	0	0	-	0
22	0	0	0	0	-	0
23	0	0	0	0	-	0
24	0	0	0	0	-	0
25	0	0	0	0	-	0
26	0	0	0	0	-	0
27	0	0	0	0	-	0
28	0	0	0	0	-	0
29	0	0	0	0	-	0
30	0	0	0	0	-	0
<b>Total Monthly Flow (MG)</b>	0	0	0	0		0
<b>Average Daily Flow (MGD)</b>	0	0	0	0		0
<b>Cumulative Annual Flow to Date (MG)</b>	0	0	0	0		0

# **Attachment C**

**MONTHLY MONITORING REPORT**

**DISCHARGER:** Morning Star Packing Company, LP and Fred Gobel

**FACILITY:** Morning Star Tomato Packing Plant

**MONTH**

April
-------

**COUNTY:** Colusa

**YEAR**

2015
------

**WDRs Order:** R5-2013-0144

**WASTEWATER MONITORING RESULTS : No Washwater Monitoring**

**Samples Collected from Station 1**

Monitoring Week	Monitoring Date	BOD (mg/L)	3-Sample Average BOD (mg/L) <sup>1</sup>	Total Nitrogen (mg/L)	3-Sample Average Total Nitrogen (mg/L) <sup>1</sup>	FDS (mg/L)
Second to Last Week of Previous Month			N/A		N/A	N/A
Last Week of Previous Month			N/A		N/A	N/A
Week 1 of Current Month						
Week 2 of Current Month						
Week 3 of Current Month						
Week 4 of Current Month						
Week 5 of Current Month						

Sampling is not required during periods when no wastewater is discharged to the LAAs.


<b>Average BOD Concentration (mg/L)<sup>1</sup></b>	
<b>Average Monthly Total Nitrogen Concentration (mg/L)<sup>2</sup></b>	
<b>Monthly Average FDS Concentration (mg/L)</b>	
<b>Flow Weighted Average FDS Concentration to Date (mg/L)<sup>3</sup></b>	

<sup>1</sup>See MRP Reporting Section A.4.

<sup>2</sup>Value to be used in annual loading calculation (WDR Section C.2.a).


<sup>3</sup>Calculated per WDR Section C.1.a (Show Calculations).

# **Attachment D**

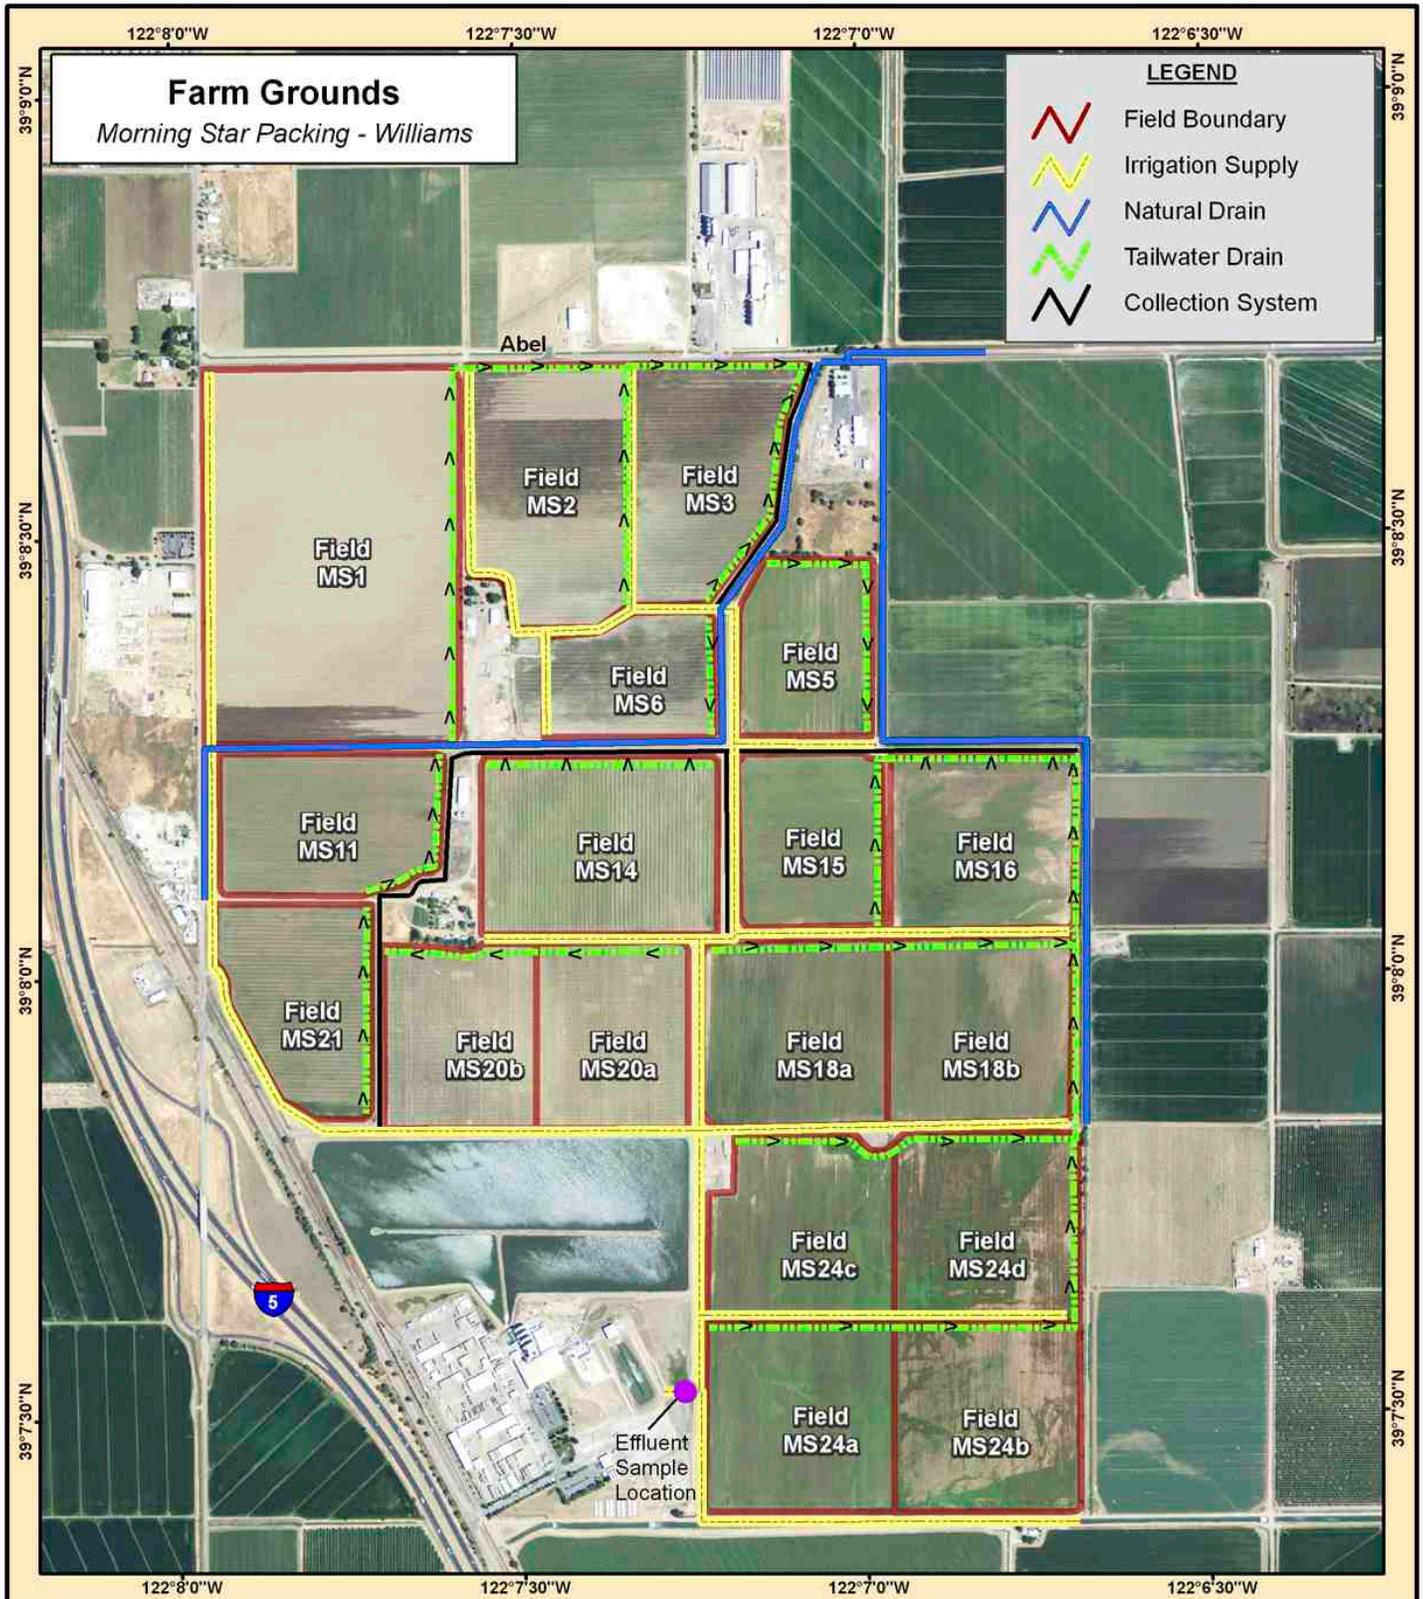

Custom Mapping Services, L.L.C. does not guarantee the accuracy or content of the data used in this map. Map is intended for pictorial use only and is not to be used for legal purposes.

Map Scale 1:14,400 1 Inch = 1,200 Feet



Data Source:  
 Aerial Photography: Summer 2012  
 Projection: UTM Zone 10N, NAD 83  
 State of California: Colusa County

Map Source:  
 Custom Mapping Services, L.L.C.  
 Prairieville, LA (225) 677-7207  
 Map Date: February 27, 2014  
 Map ID: CMS2014-038


**Farm Grounds - Field MS2**  
Morning Star Packing - Williams

Abel

**LEGEND**



-  Tarp 7 (6 checks)
-  Tarp 6 (7 checks)
-  Tarp 5 (8 checks)
-  Tarp 4 (8 checks)
-  Tarp 3 (8 checks)
-  Tarp 2 (8 checks)
-  Tarp 1 (13 checks)

-  Field Boundary
-  Irrigation Supply
-  Natural Drain
-  Tailwater Drain
-  Collection System

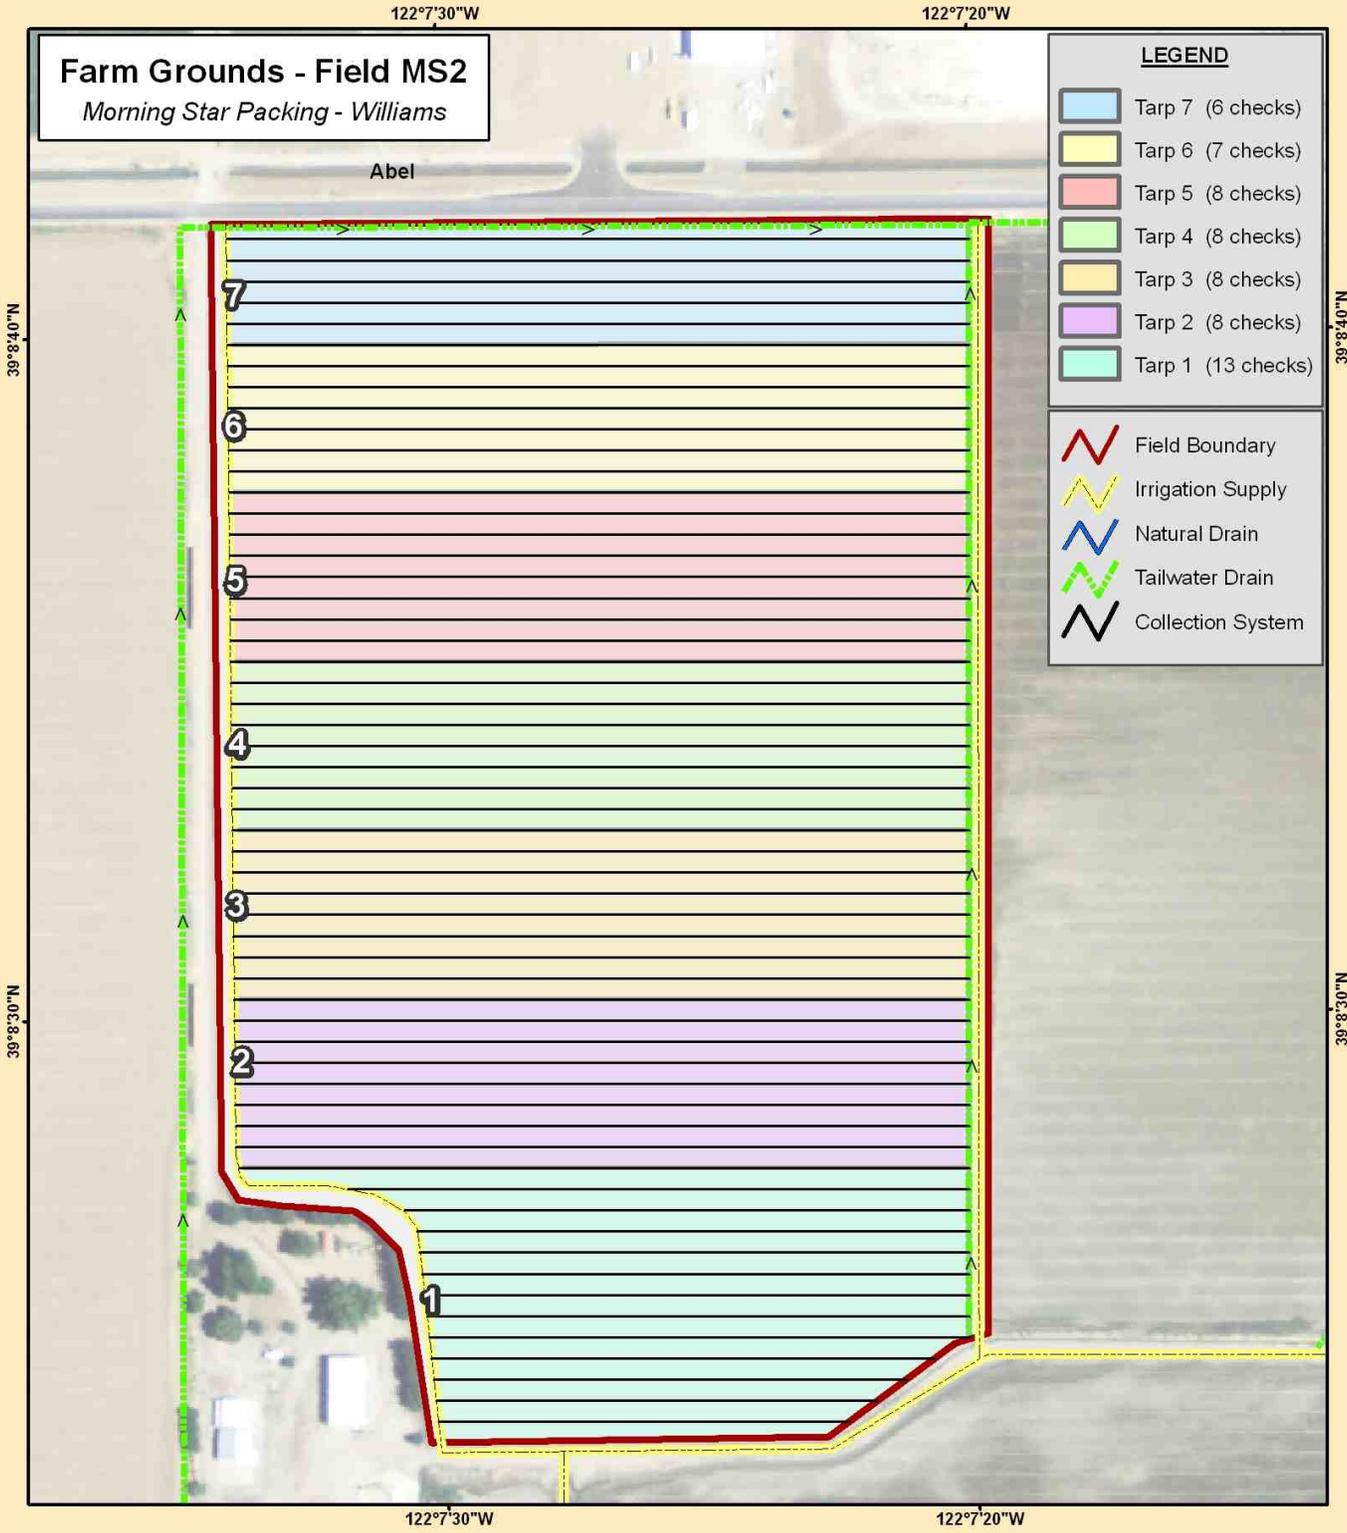

Custom Mapping Services, L.L.C. does not guarantee the accuracy or content of the data used in this map. Map is intended for pictorial use only and is not to be used for legal purposes.

Map Scale 1:3,000 1 Inch = 250 Feet




Data Source:  
Aerial Photography: Summer 2012  
Projection: UTM Zone 10N, NAD 83  
State of California: Colusa County

Map Source:  
Custom Mapping Services, L.L.C.  
Prairieville, LA (225) 677-7207  
Map Date: March 18, 2014  
Map ID: CMS2014-043

**Farm Grounds - Field MS3**  
Morning Star Packing - Williams


**LEGEND**

-  Tarp 7 (6 checks)
  -  Tarp 6 (7 checks)
  -  Tarp 5 (8 checks)
  -  Tarp 4 (8 checks)
  -  Tarp 3 (8 checks)
  -  Tarp 2 (8 checks)
  -  Tarp 1 (8 checks)
- 
-  Field Boundary
  -  Irrigation Supply
  -  Natural Drain
  -  Tailwater Drain
  -  Collection System

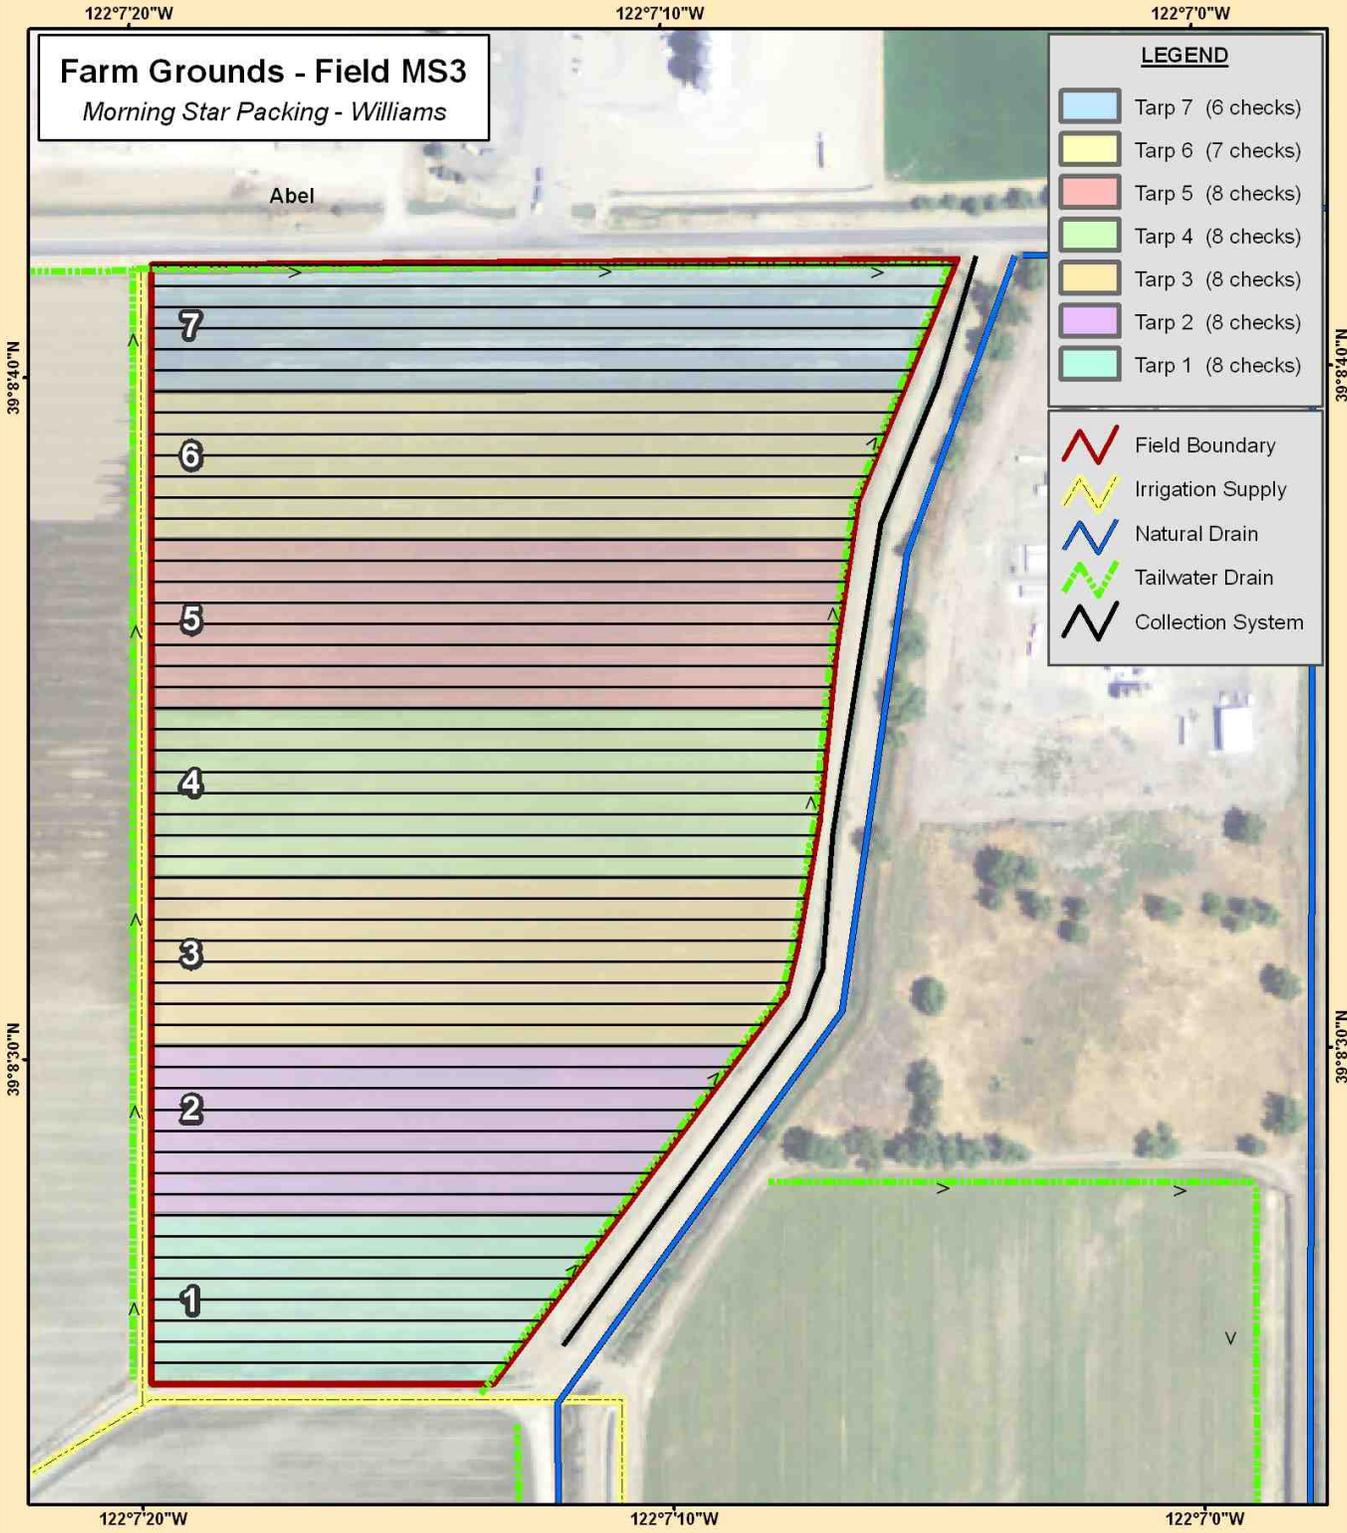

Custom Mapping Services, L.L.C. does not guarantee the accuracy or content of the data used in this map. Map is intended for pictorial use only and is not to be used for legal purposes.

Map Scale 1:3,000 1 Inch = 250 Feet



Data Source:  
Aerial Photography: Summer 2012  
Projection: UTM Zone 10N, NAD 83  
State of California: Colusa County

Map Source:  
Custom Mapping Services, L.L.C.  
Prairieville, LA (225) 677-7207  
Map Date: March 24, 2014  
Map ID: CMS2014-044

**Farm Grounds - Field MS5**  
Morning Star Packing - Williams


**LEGEND**

-  Tarp 4 (9 checks)
  -  Tarp 3 (8 checks)
  -  Tarp 2 (7 checks)
  -  Tarp 1 (7 checks)
- 
-  Field Boundary
  -  Irrigation Supply
  -  Natural Drain
  -  Tailwater Drain
  -  Collection System



Custom Mapping Services, L.L.C. does not guarantee the accuracy or content of the data used in this map. Map is intended for pictorial use only and is not to be used for legal purposes.

Map Scale 1:2,700 1 Inch = 225 Feet



Data Source:  
Aerial Photography: Summer 2012  
Projection: UTM Zone 10N, NAD 83  
State of California: Colusa County

Map Source:  
Custom Mapping Services, L.L.C.  
Prairieville, LA (225) 677-7207  
Map Date: March 24, 2014  
Map ID: CMS2014-049

**Farm Grounds - Field MS6**  
Morning Star Packing - Williams


**LEGEND**

-  Tarp 4 (7 checks)
-  Tarp 3 (7 checks)
-  Tarp 2 (7 checks)
-  Tarp 1 (8 checks)
-  Field Boundary
-  Irrigation Supply
-  Natural Drain
-  Tailwater Drain
-  Collection System



Custom Mapping Services, L.L.C. does not guarantee the accuracy or content of the data used in this map. Map is intended for pictorial use only and is not to be used for legal purposes.

Map Scale 1:2,700 1 Inch = 225 Feet



Data Source:  
Aerial Photography: Summer 2012  
Projection: UTM Zone 10N, NAD 83  
State of California: Colusa County


Map Source:  
Custom Mapping Services, L.L.C.  
Prairieville, LA (225) 677-7207  
Map Date: March 24, 2014  
Map ID: CMS2014-047

**Farm Grounds - Field MS11**  
*Morning Star Packing - Williams*

**LEGEND**



-  Tarp 4 (9 checks)
-  Tarp 3 (8 checks)
-  Tarp 2 (8 checks)
-  Tarp 1 (7 checks)

-  Field Boundary
-  Irrigation Supply
-  Natural Drain
-  Tailwater Drain
-  Collection System

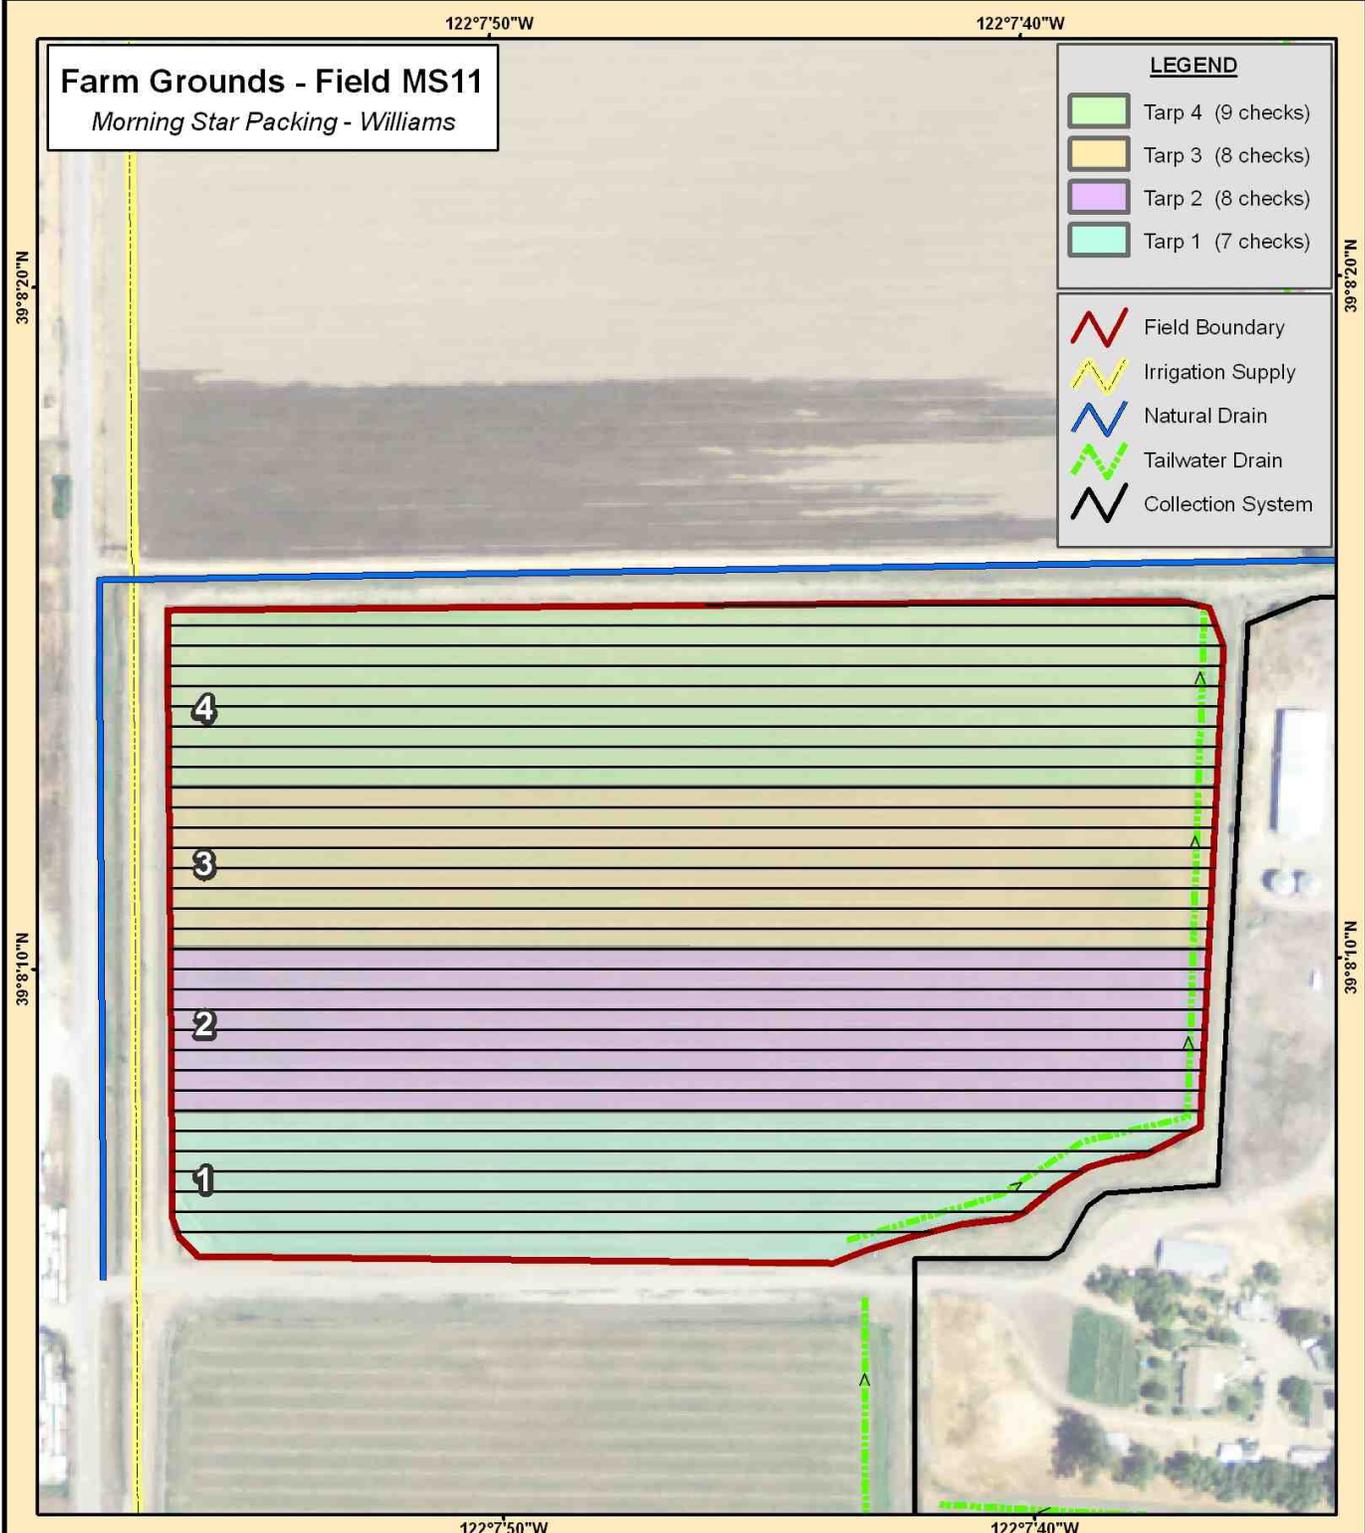

*Custom Mapping Services, L.L.C. does not guarantee the accuracy or content of the data used in this map. Map is intended for pictorial use only and is not to be used for legal purposes.*

Map Scale 1:3,000 1 Inch = 250 Feet



Data Source:  
 Aerial Photography: Summer 2012  
 Projection: UTM Zone 10N, NAD 83  
 State of California: Colusa County




Map Source:  
 Custom Mapping Services, L.L.C.  
 Prairieville, LA (225) 677-7207  
 Map Date: March 24, 2014  
 Map ID: CMS2014-048

**Farm Grounds - Field MS14**  
Morning Star Packing - Williams

**LEGEND**


-  Tarp 7 (6 checks)
-  Tarp 6 (8 checks)
-  Tarp 5 (8 checks)
-  Tarp 4 (8 checks)
-  Tarp 3 (8 checks)
-  Tarp 2 (8 checks)
-  Tarp 1 (8 checks)

-  Field Boundary
-  Irrigation Supply
-  Natural Drain
-  Tailwater Drain
-  Collection System

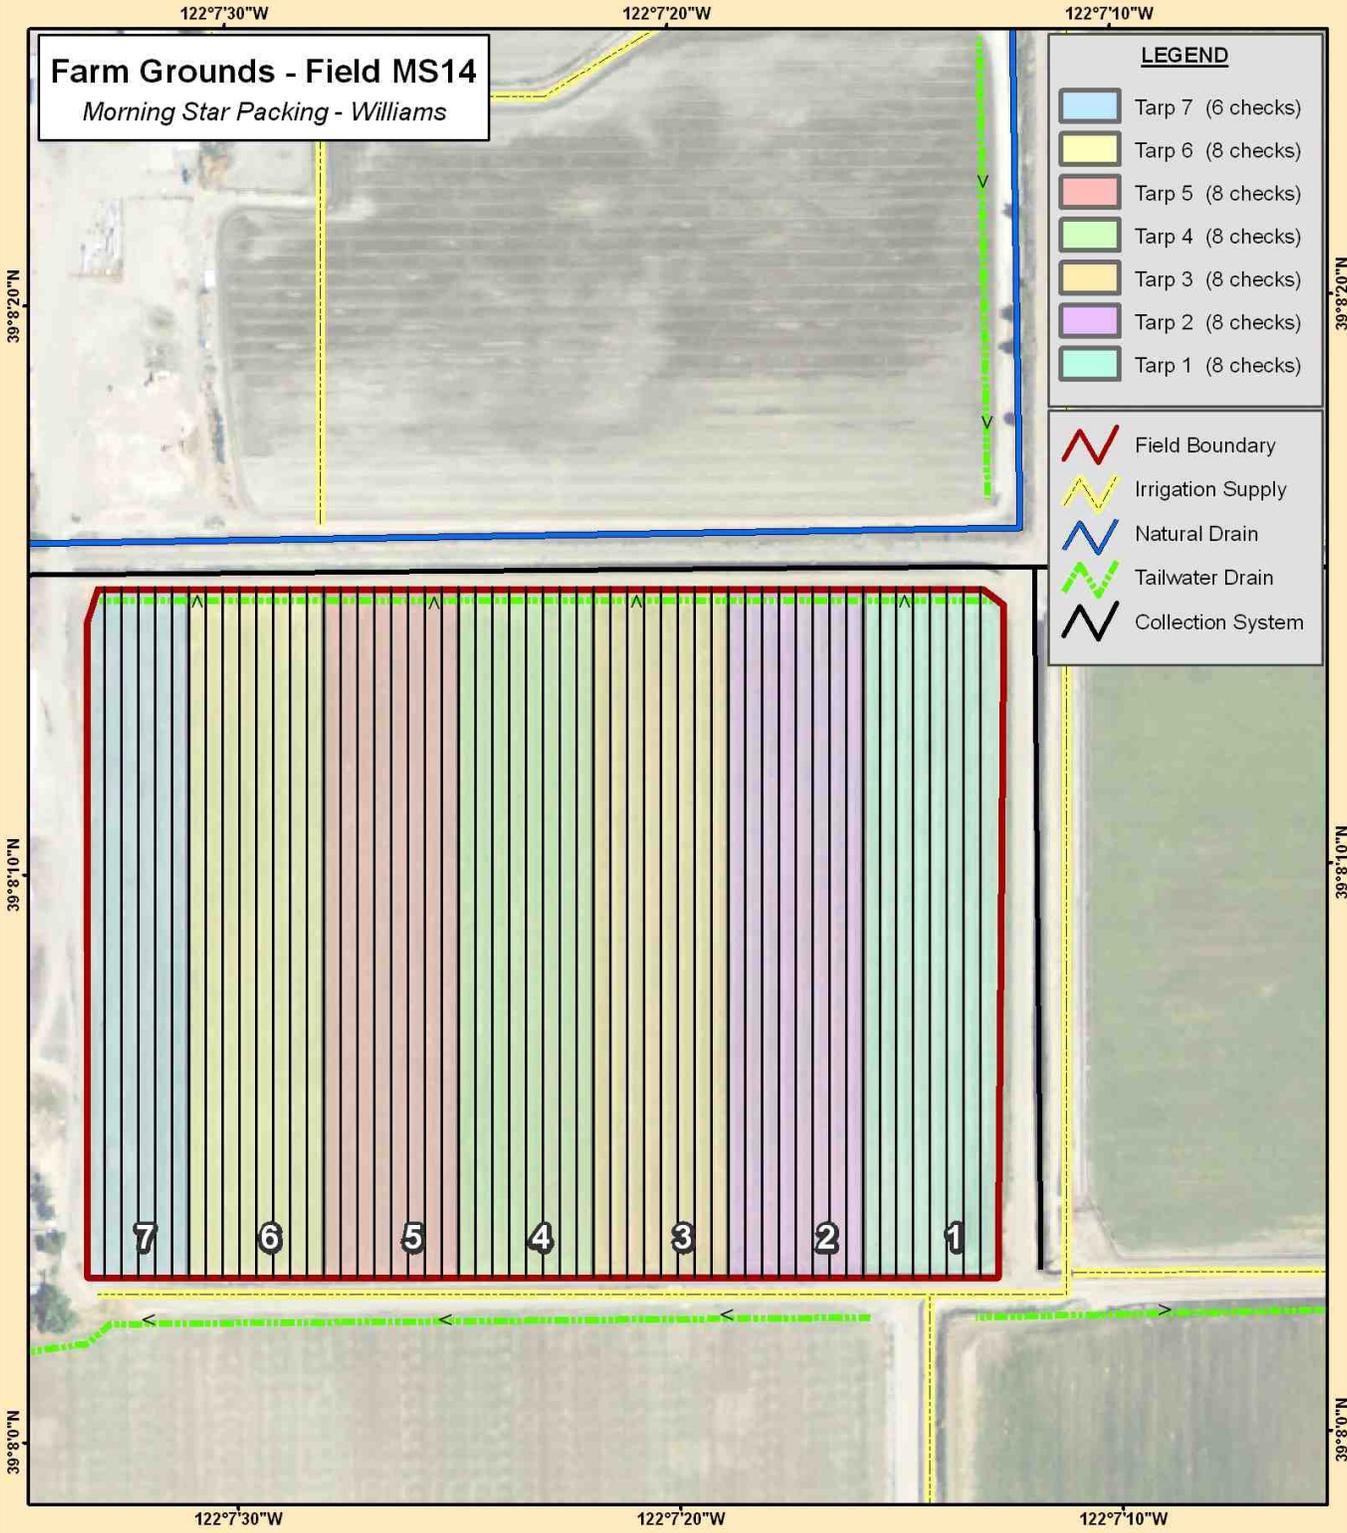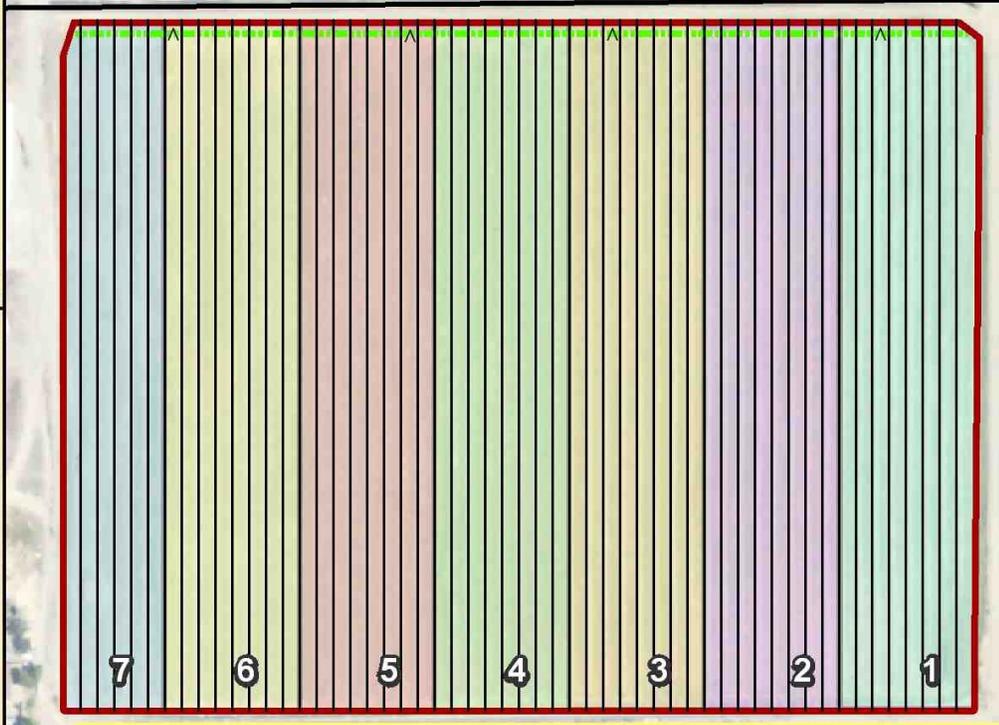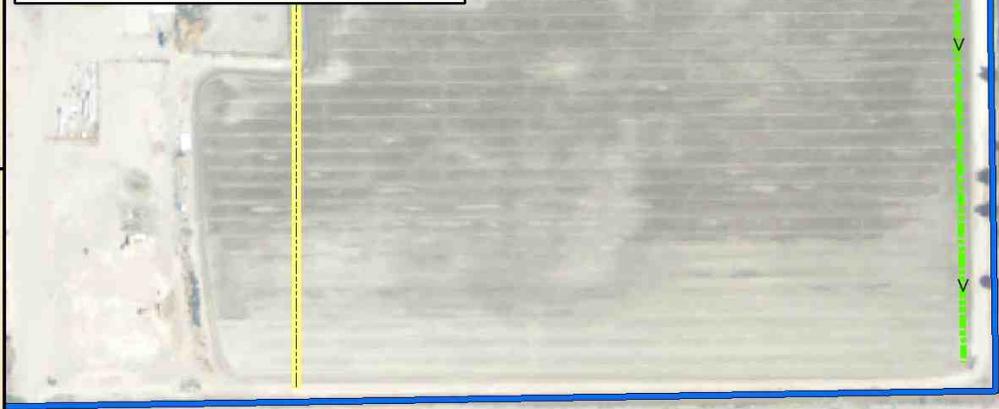

Custom Mapping Services, L.L.C. does not guarantee the accuracy or content of the data used in this map. Map is intended for pictorial use only and is not to be used for legal purposes.

Map Scale 1:3,600 1 Inch = 300 Feet



Data Source:  
Aerial Photography: Summer 2012  
Projection: UTM Zone 10N, NAD 83  
State of California: Colusa County

Map Source:  
Custom Mapping Services, L.L.C.  
Prairieville, LA (225) 677-7207  
Map Date: March 24, 2014  
Map ID: CMS2014-050


**Farm Grounds - Field MS15**  
Morning Star Packing - Williams

**LEGEND**

-  Tarp 4 (9 checks)
-  Tarp 3 (12 checks)
-  Tarp 2 (11 checks)
-  Tarp 1 (8 checks)

-  Field Boundary
-  Irrigation Supply
-  Natural Drain
-  Tailwater Drain
-  Collection System

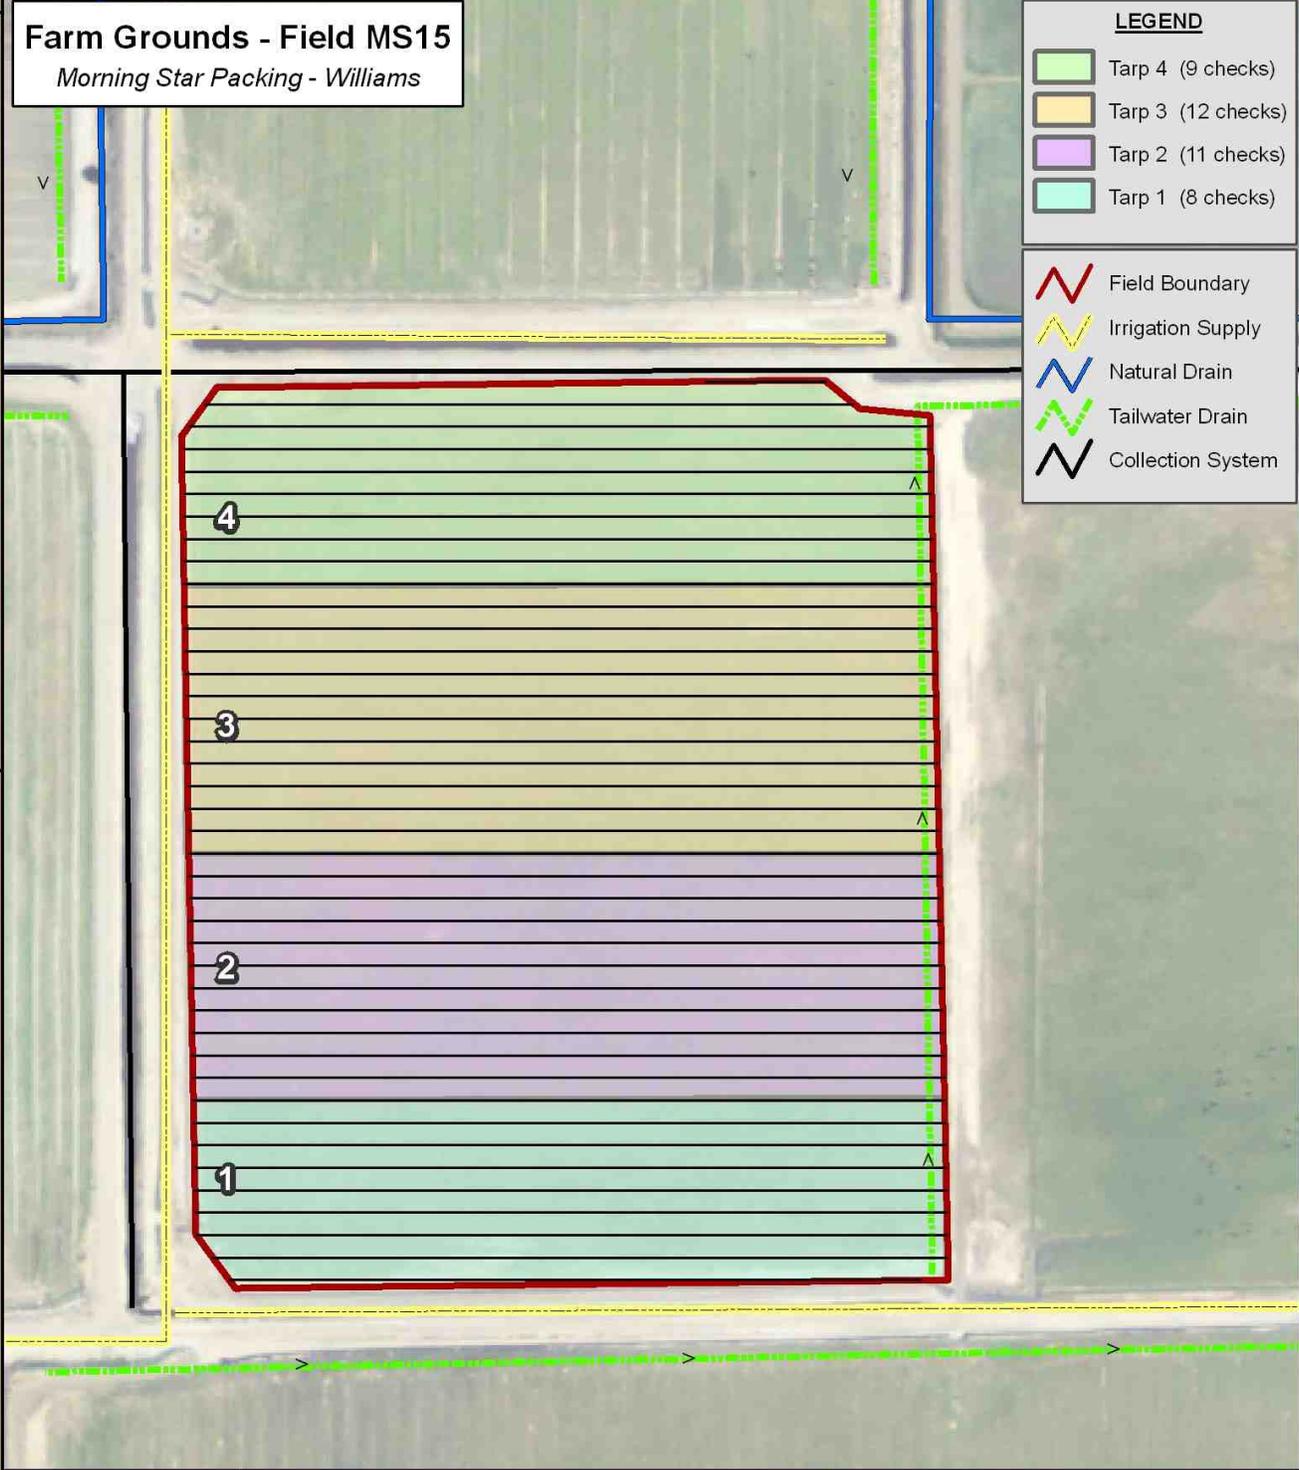

Custom Mapping Services, L.L.C. does not guarantee the accuracy or content of the data used in this map. Map is intended for pictorial use only and is not to be used for legal purposes.

Map Scale 1:2,700 1 Inch = 225 Feet




Data Source:  
Aerial Photography: Summer 2012  
Projection: UTM Zone 10N, NAD 83  
State of California: Colusa County

Map Source:  
Custom Mapping Services, L.L.C.  
Prairieville, LA (225) 677-7207  
Map Date: March 24, 2014  
Map ID: CMS2014-045

**Farm Grounds - Field MS20a & 20b**  
*Morning Star Packing - Williams*



-  Field Boundary
-  Irrigation Supply
-  Natural Drain
-  Tailwater Drain
-  Collection System

LEGEND	
	Tarp 5b (7 checks)
	Tarp 4b (6 checks)
	Tarp 3b (7 checks)
	Tarp 2b (7 checks)
	Tarp 1b (7 checks)
	Tarp 5a (7 checks)
	Tarp 4a (7 checks)
	Tarp 3a (7 checks)
	Tarp 2a (6 checks)
	Tarp 1a (8 checks)

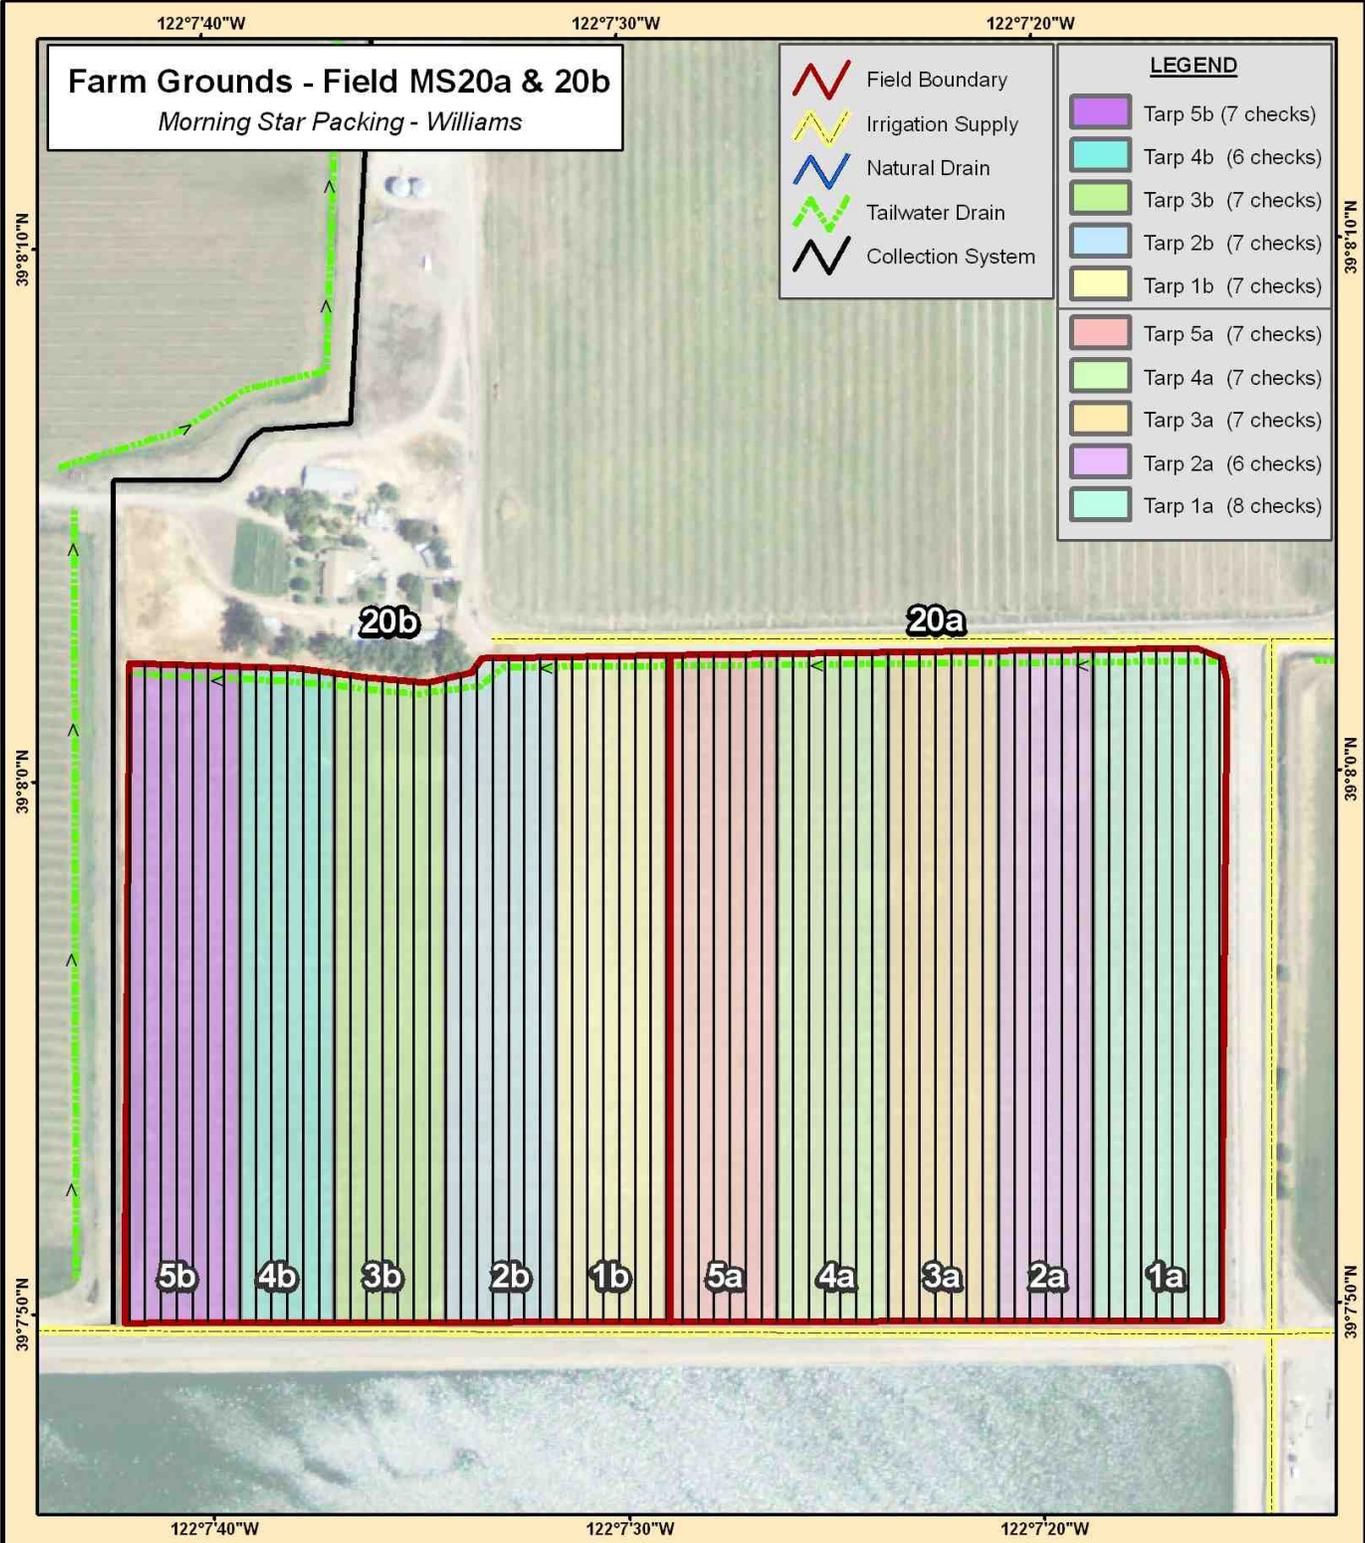

*Custom Mapping Services, L.L.C. does not guarantee the accuracy or content of the data used in this map. Map is intended for pictorial use only and is not to be used for legal purposes.*

Map Scale 1:3,840 1 Inch = 320 Feet



Data Source:  
 Aerial Photography: Summer 2012  
 Projection: UTM Zone 10N, NAD 83  
 State of California: Colusa County


Map Source:  
 Custom Mapping Services, L.L.C.  
 Prairieville, LA (225) 677-7207  
 Map Date: March 24, 2014  
 Map ID: CMS2014-051

**Farm Grounds - Field MS21**  
Morning Star Packing - Williams

**LEGEND**


-  Tarp 7 (7 checks)
-  Tarp 6 (7 checks)
-  Tarp 5 (7 checks)
-  Tarp 4 (7 checks)
-  Tarp 3 (7 checks)
-  Tarp 2 (7 checks)
-  Tarp 1 (8 checks)

-  Field Boundary
-  Irrigation Supply
-  Natural Drain
-  Tailwater Drain
-  Collection System

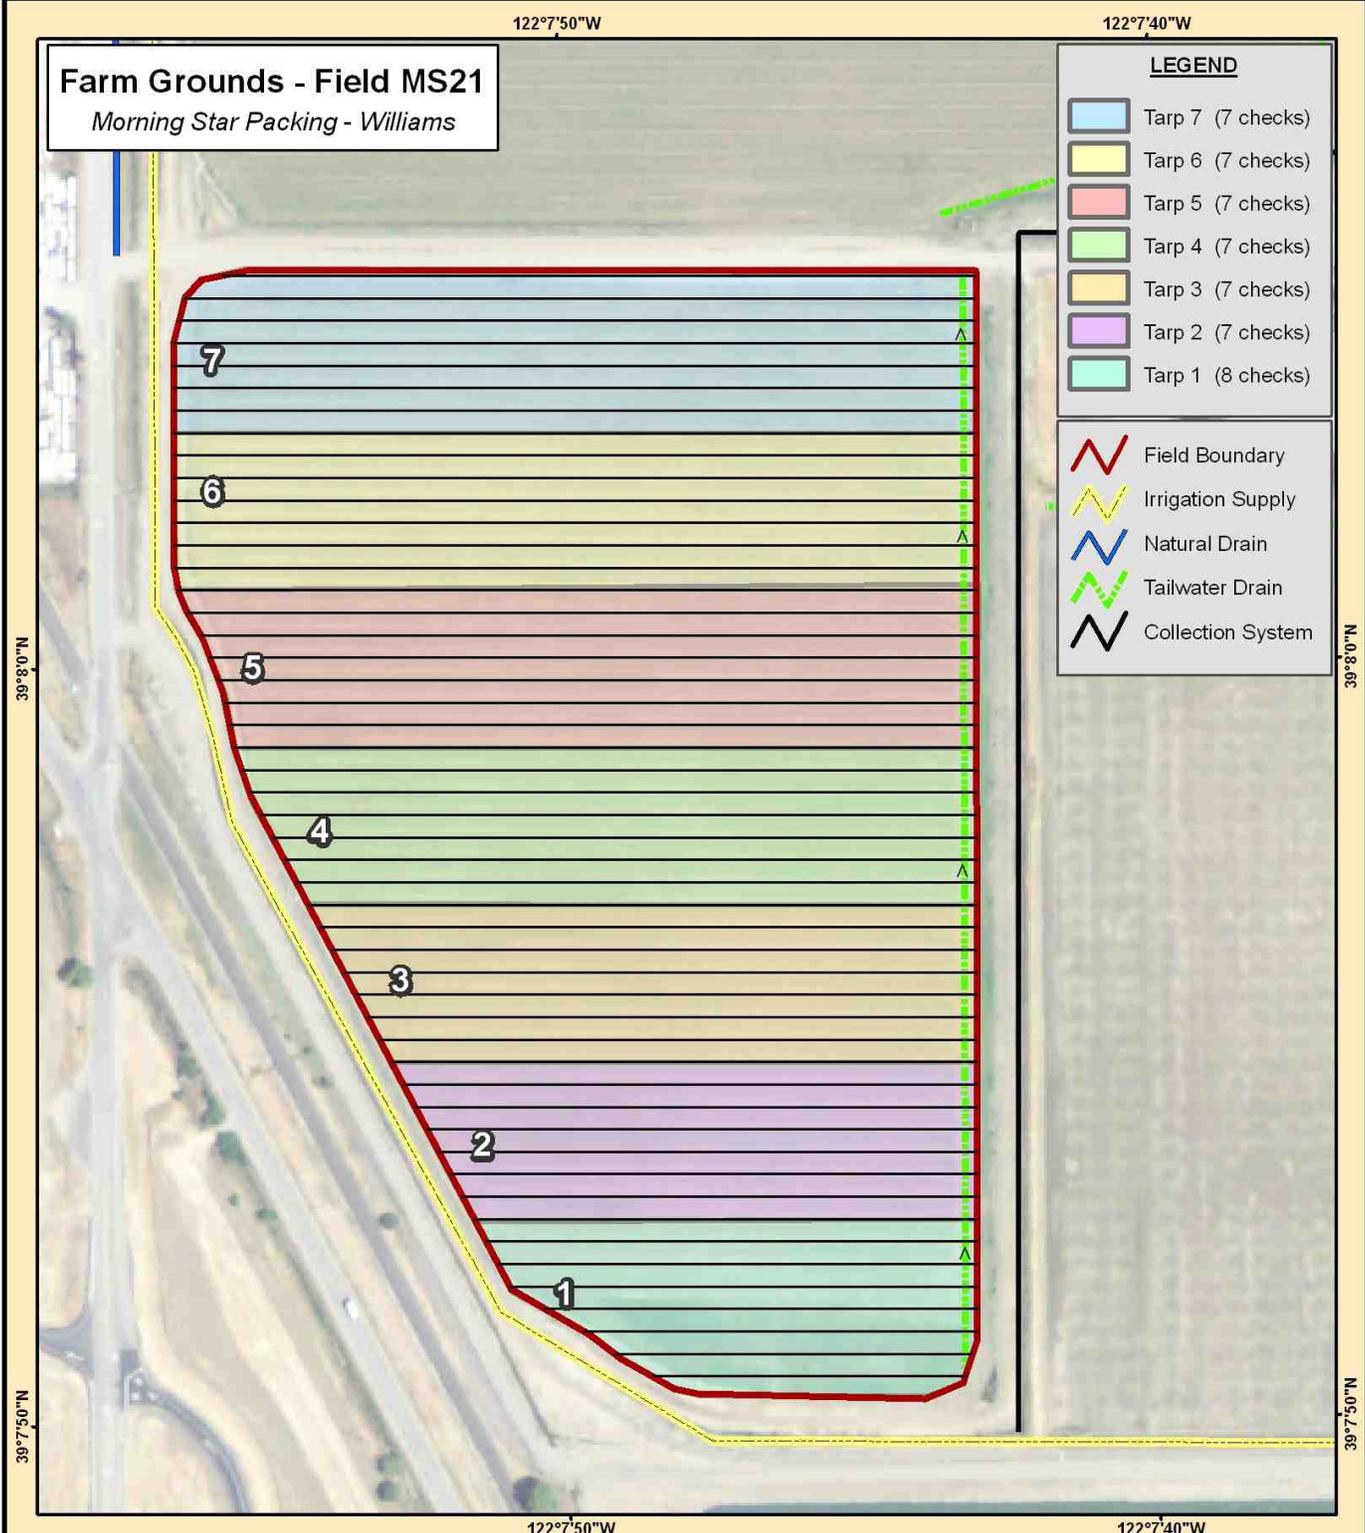

Custom Mapping Services, L.L.C. does not guarantee the accuracy or content of the data used in this map. Map is intended for pictorial use only and is not to be used for legal purposes.

Map Scale 1:2,700 1 Inch = 225 Feet



Data Source:  
Aerial Photography: Summer 2012  
Projection: UTM Zone 10N, NAD 83  
State of California: Colusa County

Map Source:  
Custom Mapping Services, L.L.C.  
Prairieville, LA (225) 677-7207  
Map Date: March 24, 2014  
Map ID: CMS2014-046

# **Attachment E**

**MONTHLY MONITORING REPORT**

MONTH April  
 YEAR 2015

DISCHARGER: Morning Star Packing Company, LP and Fred Gobel  
 FACILITY: Morning Star Tomato Packing Plant  
 COUNTY: Colusa  
 WDRs Order: R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

MS2

(Submit one sheet for each field irrigated during the month)

Field Irrigation Information

Area (acres)	41.05
Number of Checks	58
Check Width (feet)	30
Check Length (feet)**	1,100
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

Crop Information

Crop Name	Oats
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	12/1/14
Actual Planting Date	12/3/14
Anticipated Harvest Date	April/May 2015
Actual Harvest Date	5/5/15
Expected Harvest Yield	3-3.5 tons/acre
Actual Harvest Yield	1 ton/acre

Cattle Grazing Schedule

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

\*\*Est based on Google Earth

\*Stormwater not allowed to drain and ruined seeds.

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Total Volume to Each Check (gal)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
31										
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

**Total Nitrogen Loading Rate for Month (lb/ac)<sup>3</sup>** 0

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

MONTH 

April
-------

  
 YEAR 

2015
------

DISCHARGER: Morning Star Packing Company, LP and Fred Gobel  
 FACILITY: Morning Star Tomato Packing Plant  
 COUNTY: Colusa  
 WDRs Order: R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

(Submit one sheet for each field irrigated during the month)

**Field Irrigation Information**

Area (acres)	41.05
Number of Checks	53
Check Width (feet)	30
Check Length (feet)**	1,000
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

\*\*Est based on Google Earth

MS3

**Crop Information**

Crop Name	Oats
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	12/1/14
Actual Planting Date	12/3/14
Anticipated Harvest Date	April/May 2015
Actual Harvest Date	5/5/15
Expected Harvest Yield	3-3.5 tons/acre
Actual Harvest Yield	1 ton/acre

\*Stormwater not allowed to drain and ruined seeds.

**Cattle Grazing Schedule**

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
31										
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

**Total Nitrogen Loading Rate for Month (lb/ac)<sup>3</sup>**

0
---

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

MONTH 

April
-------

  
 YEAR 

2015
------

DISCHARGER: Morning Star Packing Company, LP and Fred Gobel  
 FACILITY: Morning Star Tomato Packing Plant  
 COUNTY: Colusa  
 WDRs Order: R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

MS5

(Submit one sheet for each field irrigated during the month)

**Field Irrigation Information**

Area (acres)	24.6
Number of Checks	34
Check Width (feet)	30
Check Length (feet)**	1,200
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

**Crop Information**

Crop Name	Oats
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	12/1/14
Actual Planting Date	12/3/14
Anticipated Harvest Date	April/May 2015
Actual Harvest Date	
Expected Harvest Yield	3-3.5 tons/acre
Actual Harvest Yield	1.5 tons/acre

**Cattle Grazing Schedule**

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

\*\*Est based on Google Earth

\*Stormwater not allowed to drain and ruined seeds.

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

Total Nitrogen Loading Rate for Month (lb/ac) <sup>3</sup>	0
--	---

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

MONTH 

April
-------

  
 YEAR 

2015
------

DISCHARGER: Morning Star Packing Company, LP and Fred Gobel  
 FACILITY: Morning Star Tomato Packing Plant  
 COUNTY: Colusa  
 WDRs Order: R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

MS6

(Submit one sheet for each field irrigated during the month)

**Field Irrigation Information**

Area (acres)	21.4
Number of Checks	29
Check Width (feet)	30
Check Length (feet)**	1,300
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

**Crop Information**

Crop Name	Oats
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	12/1/14
Actual Planting Date	12/3/14
Anticipated Harvest Date	April/May 2015
Actual Harvest Date	
Expected Harvest Yield	3-3.5 tons/acre
Actual Harvest Yield	0 ton/acre

**Cattle Grazing Schedule**

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

\*\*Est based on Google Earth

\*Stormwater not allowed to drain and ruined seeds.

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0							
6			0							
7			0							
8			0							
9			0							
10			0							
11			0.15							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0.06							
23			0							
24			0							
25			0							
26			0							
27			0							
28			0							
29			0							
30			0							
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

Total Nitrogen Loading Rate for Month (lb/ac)<sup>3</sup>

0
---

<sup>3</sup>See MRP footnote 5

MONTHLY MONITORING REPORT

MONTH   
 YEAR

DISCHARGER: Morning Star Packing Company, LP and Fred Gobel  
 FACILITY: Morning Star Tomato Packing Plant  
 COUNTY: Colusa  
 WDRs Order: R5-2013-0144

LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME

(Submit one sheet for each field irrigated during the month)

Field Irrigation Information

Area (acres)	<input type="text" value="35.6"/>
Number of Checks	<input type="text" value="32"/>
Check Width (feet)	<input type="text" value="30"/>
Check Length (feet)**	<input type="text" value="1,500"/>
Irrigation Application Days	<input type="text" value="N/A"/>
Irrigation Resting Days	<input type="text" value="N/A"/>
Irrigation Cycle Days	<input type="text" value="N/A"/>

\*\*Est based on Google Earth

Crop Information

Crop Name	<input type="text" value="Oats"/>
Crop ET (Inches)	<input type="text"/>
Total Nitrogen Demand (lb/ac)	<input type="text"/>
Anticipated Planting Date	<input type="text" value="12/1/14"/>
Actual Planting Date	<input type="text" value="12/3/14"/>
Anticipated Harvest Date	<input type="text" value="April/May 2015"/>
Actual Harvest Date	<input type="text" value="5/6/15"/>
Expected Harvest Yield	<input type="text" value="3-3.5 tons/acre"/>
Actual Harvest Yield	<input type="text" value="2.1 tons/acre"/>

Cattle Grazing Schedule

Number of Cattle on Field	<input type="text" value="0"/>
Cattle Grazing Start Date	<input type="text" value="N/A"/>
Cattle Grazing End Date	<input type="text" value="N/A"/>
BOD Mass/Head (lb/day/head)	<input type="text" value="N/A"/>
Nitrogen Mass/Head (lb/day/head)	<input type="text" value="N/A"/>

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

Total Nitrogen Loading Rate for Month (lb/ac) <sup>3</sup>	<input type="text" value="0"/>
--	--------------------------------

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

MONTH 

April
-------

  
 YEAR 

2015
------

DISCHARGER: Morning Star Packing Company, LP and Fred Gobel  
 FACILITY: Morning Star Tomato Packing Plant  
 COUNTY: Colusa  
 WDRs Order: R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

**MS14**

(Submit one sheet for each field irrigated during the month)

**Field Irrigation Information**

Area (acres)	44.5
Number of Checks	54
Check Width (feet)	30
Check Length (feet)**	1,250
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

\*\*Est based on Google Earth

**Crop Information**

Crop Name	Oats
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	12/1/14
Actual Planting Date	12/3/14
Anticipated Harvest Date	April/May 2015
Actual Harvest Date	5/4/15
Expected Harvest Yield	2-2.5 tons/acre
Actual Harvest Yield	2.4 tons/acre

**Cattle Grazing Schedule**

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

<b>Total Nitrogen Loading Rate for Month (lb/ac)<sup>3</sup></b>	0
--	---

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

MONTH	April
YEAR	2015

**DISCHARGER:** Morning Star Packing Company, LP and Fred Gobel  
**FACILITY:** Morning Star Tomato Packing Plant  
**COUNTY:** Colusa  
**WDRs Order:** R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

**MS15**

(Submit one sheet for each field irrigated during the month)

**Field Irrigation Information**

Area (acres)	26.7
Number of Checks	40
Check Width (feet)	30
Check Length (feet)**	1,000
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

\*\*Est based on Google Earth

**Crop Information**

Crop Name	Oats
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	12/1/14
Actual Planting Date	12/3/14
Anticipated Harvest Date	April/May 2015
Actual Harvest Date	
Expected Harvest Yield	3-3.5 tons/acre
Actual Harvest Yield	1.2 tons/acre

\*Stormwater not allowed to drain and ruined seeds.

**Cattle Grazing Schedule**

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

<b>Total Nitrogen Loading Rate for Month (lb/ac)<sup>3</sup></b>	0
--	---

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

MONTH 

April
-------

  
 YEAR 

2015
------

DISCHARGER: Morning Star Packing Company, LP and Fred Gobel  
 FACILITY: Morning Star Tomato Packing Plant  
 COUNTY: Colusa  
 WDRs Order: R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

MS16

(Submit one sheet for each field irrigated during the month)

Field Irrigation Information

Area (acres)	36.7
Number of Checks	*42
Check Width (feet)	30
Check Length (feet)**	1,240
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

\*Estimated & Calculated based on Google Earth with 30' checks  
 \*\*Est based on Google Earth

Crop Information

Crop Name	Oats
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	12/1/14
Actual Planting Date	12/3/14
Anticipated Harvest Date	April/May 2015
Actual Harvest Date	
Expected Harvest Yield	3-3.5 tons/acre
Actual Harvest Yield	1 ton/acre

\*Stormwater not allowed to drain and ruined seeds.

Cattle Grazing Schedule

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

Total Nitrogen Loading Rate for Month (lb/ac)<sup>3</sup>

0
---

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

MONTH 

April
-------

  
 YEAR 

2015
------

**DISCHARGER:** Morning Star Packing Company, LP and Fred Gobel  
**FACILITY:** Morning Star Tomato Packing Plant  
**COUNTY:** Colusa  
**WDRs Order:** R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

(Submit one sheet for each field irrigated during the month)

MS18a

Field Irrigation Information

Area (acres)	39.1
Number of Checks*	42
Check Width (feet)	30
Check Length (feet)**	1,300
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

Crop Information

Crop Name	Oats
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	12/1/14
Actual Planting Date	12/3/14
Anticipated Harvest Date	April/May 2015
Actual Harvest Date	
Expected Harvest Yield	3-3.5 tons/acre
Actual Harvest Yield	3 tons/acre

Cattle Grazing Schedule

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

\*Estimated & Calculated based on Google Earth with 30' checks  
 \*\*Est based on Google Earth

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

**Total Nitrogen Loading Rate for Month (lb/ac)<sup>3</sup>**

0
---

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

MONTH 

April
-------

  
 YEAR 

2015
------

**DISCHARGER:** Morning Star Packing Company, LP and Fred Gobel  
**FACILITY:** Morning Star Tomato Packing Plant  
**COUNTY:** Colusa  
**WDRs Order:** R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

<b>MS18b</b>
--------------

(Submit one sheet for each field irrigated during the month)

**Field Irrigation Information**

Area (acres)	39.1
Number of Checks*	43
Check Width (feet)	30
Check Length (feet)**	1,300
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

**Crop Information**

Crop Name	Oats
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	12/1/14
Actual Planting Date	12/3/14
Anticipated Harvest Date	April/May 2015
Actual Harvest Date	
Expected Harvest Yield	3-3.5 tons/acre
Actual Harvest Yield	3 tons/acre

**Cattle Grazing Schedule**

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

\*Estimated & Calculated based on Google Earth with 30' checks  
 \*\*Est based on Google Earth

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

<b>Total Nitrogen Loading Rate for Month (lb/ac)<sup>3</sup></b>	0
--	---

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

MONTH 

April
-------

  
 YEAR 

2015
------

**DISCHARGER:** Morning Star Packing Company, LP and Fred Gobel  
**FACILITY:** Morning Star Tomato Packing Plant  
**COUNTY:** Colusa  
**WDRs Order:** R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

(Submit one sheet for each field irrigated during the month)

MS20a

**Field Irrigation Information**

Area (acres)	32.3
Number of Checks	34
Check Width (feet)	30
Check Length (feet)**	1,250
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

\*\*Est based on Google Earth

**Crop Information**

Crop Name	Oats
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	12/1/14
Actual Planting Date	12/3/14
Anticipated Harvest Date	April/May 2015
Actual Harvest Date	5/6/15
Expected Harvest Yield	3-3.5 tons/acre
Actual Harvest Yield	1.5 tons/acre

\*Stormwater not allowed to drain and ruined seeds.

**Cattle Grazing Schedule**

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

**Total Nitrogen Loading Rate for Month (lb/ac)<sup>3</sup>**

0
---

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

**MONTH**

April
-------

  
**YEAR**

2015
------

**DISCHARGER:** Morning Star Packing Company, LP and Fred Gobel  
**FACILITY:** Morning Star Tomato Packing Plant  
**COUNTY:** Colusa  
**WDRs Order:** R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

MS20b

(Submit one sheet for each field irrigated during the month)

**Field Irrigation Information**

Area (acres)	32.3
Number of Checks	35
Check Width (feet)	30
Check Length (feet)**	1,250
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

\*\*Est based on Google Earth

**Crop Information**

Crop Name	Oats
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	12/1/14
Actual Planting Date	12/3/14
Anticipated Harvest Date	April/May 2015
Actual Harvest Date	5/6/15
Expected Harvest Yield	3-3.5 tons/acre
Actual Harvest Yield	1.1 tons/acre

\*Stormwater not allowed to drain and ruined seeds.

**Cattle Grazing Schedule**

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

<b>Total Nitrogen Loading Rate for Month (lb/ac)<sup>3</sup></b>	0
--	---

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

**MONTH**

April
-------

  
**YEAR**

2015
------

**DISCHARGER:** Morning Star Packing Company, LP and Fred Gobel  
**FACILITY:** Morning Star Tomato Packing Plant  
**COUNTY:** Colusa  
**WDRs Order:** R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

MS21

(Submit one sheet for each field irrigated during the month)

Field Irrigation Information

Area (acres)	25.9
Number of Checks	50
Check Width (feet)	30
Check Length (feet)**	750
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

\*\*Est based on Google Earth

Crop Information

Crop Name	Oats
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	12/1/14
Actual Planting Date	12/3/14
Anticipated Harvest Date	April/May 2015
Actual Harvest Date	
Expected Harvest Yield	3-3.5 tons/acre
Actual Harvest Yield	1 ton/acre

\*Stormwater not allowed to drain and ruined seeds.

Cattle Grazing Schedule

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

<b>Total Nitrogen Loading Rate for Month (lb/ac)<sup>3</sup></b>	0
--	---

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

MONTH 

April
-------

  
 YEAR 

2015
------

DISCHARGER: Morning Star Packing Company, LP and Fred Gobel  
 FACILITY: Morning Star Tomato Packing Plant  
 COUNTY: Colusa  
 WDRs Order: R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

**MS24a**

(Submit one sheet for each field irrigated during the month)

**Field Irrigation Information**

Area (acres)	39.95
Number of Checks*	44
Check Width (feet)	30
Check Length (feet)**	1,300
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

**Crop Information**

Crop Name	N/A
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	
Actual Planting Date	
Anticipated Harvest Date	
Actual Harvest Date	
Expected Harvest Yield	
Actual Harvest Yield	

**Cattle Grazing Schedule**

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

\*Estimated & Calculated based on Google Earth with 30' checks  
 \*\*Est based on Google Earth

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
31										
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

<b>Total Nitrogen Loading Rate for Month (lb/ac)<sup>3</sup></b>	0
--	---

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

MONTH April  
 YEAR 2015

DISCHARGER: Morning Star Packing Company, LP and Fred Gobel  
 FACILITY: Morning Star Tomato Packing Plant  
 COUNTY: Colusa  
 WDRs Order: R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

MS24b

(Submit one sheet for each field irrigated during the month)

**Field Irrigation Information**

Area (acres)	39.95
Number of Checks*	44
Check Width (feet)	30
Check Length (feet)**	1,300
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

**Crop Information**

Crop Name	N/A
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	
Actual Planting Date	
Anticipated Harvest Date	
Actual Harvest Date	
Expected Harvest Yield	
Actual Harvest Yield	

**Cattle Grazing Schedule**

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

\*Estimated & Calculated based on Google Earth with 30' checks  
 \*\*Est based on Google Earth

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
31										
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

**Total Nitrogen Loading Rate for Month (lb/ac)<sup>3</sup>** 0

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

MONTH 

April
-------

  
 YEAR 

2015
------

DISCHARGER: Morning Star Packing Company, LP and Fred Gobel  
 FACILITY: Morning Star Tomato Packing Plant  
 COUNTY: Colusa  
 WDRs Order: R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

**MS24c**

(Submit one sheet for each field irrigated during the month)

**Field Irrigation Information**

Area (acres)	39.95
Number of Checks*	44
Check Width (feet)	30
Check Length (feet)**	1,300
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

**Crop Information**

Crop Name	N/A
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	
Actual Planting Date	
Anticipated Harvest Date	
Actual Harvest Date	
Expected Harvest Yield	
Actual Harvest Yield	

**Cattle Grazing Schedule**

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

\*Estimated & Calculated based on Google Earth with 30' checks  
 \*\*Est based on Google Earth

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
31										
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

<b>Total Nitrogen Loading Rate for Month (lb/ac)<sup>3</sup></b>	0
--	---

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

MONTH 

April
-------

  
 YEAR 

2015
------

DISCHARGER: Morning Star Packing Company, LP and Fred Gobel  
 FACILITY: Morning Star Tomato Packing Plant  
 COUNTY: Colusa  
 WDRs Order: R5-2013-0144

**LAND APPLICATION AREA MONITORING RESULTS FOR FIELD NAME**

MS24d

(Submit one sheet for each field irrigated during the month)

Field Irrigation Information

Area (acres)	39.95
Number of Checks*	44
Check Width (feet)	30
Check Length (feet)**	1,300
Irrigation Application Days	N/A
Irrigation Resting Days	N/A
Irrigation Cycle Days	N/A

Crop Information

Crop Name	N/A
Crop ET (Inches)	
Total Nitrogen Demand (lb/ac)	
Anticipated Planting Date	
Actual Planting Date	
Anticipated Harvest Date	
Actual Harvest Date	
Expected Harvest Yield	
Actual Harvest Yield	

Cattle Grazing Schedule

Number of Cattle on Field	0
Cattle Grazing Start Date	N/A
Cattle Grazing End Date	N/A
BOD Mass/Head (lb/day/head)	N/A
Nitrogen Mass/Head (lb/day/head)	N/A

\*Estimated & Calculated based on Google Earth with 30' checks  
 \*\*Est based on Google Earth

Day of Month	Start Time	End Time	Precipitation (Inches)	Names of Checks Irrigated Each Day	Types of Water Applied (wastewater, cooling water, supplemental irrigation)	Estimated Flow Rate to Each Check (gpm)	Total Irrigation Hours for Each Check	Area (acres)	Total Volume of Water Applied to Each Check (inches) <sup>1</sup>	BOD Loading Rate as an Irrigation Cycle Average (lb/ac/day) <sup>2</sup>
1			0							
2			0							
3			0							
4			0							
5			0.05							
6			0							
7			0.83							
8			0							
9			0							
10			0							
11			0							
12			0							
13			0							
14			0							
15			0							
16			0							
17			0							
18			0							
19			0							
20			0							
21			0							
22			0							
23			0							
24			0.18							
25			0.05							
26			0							
27			0							
28			0							
29			0							
30			0							
31										
<b>Total</b>			1.11							

<sup>1</sup>Calculations and assumptions shall be documented on a separate piece of paper

<sup>2</sup>See MRP page 3, "Land Application Area" footnote 4 for calculation instructions. Calculations and assumptions shall be documented on a separate piece of paper.

Total Nitrogen Loading Rate for Month (lb/ac) <sup>3</sup>	0
--	---

<sup>3</sup>See MRP footnote 5

**MONTHLY MONITORING REPORT**

**DISCHARGER: Moring Star Packing Company, LP and Fred Gobel**  
**FACILITY: Morning Star Tomato Packing Plant**  
**COUNTY: Colusa**  
**WDRs Order R5-2013-0144**

**MONTH**

April
-------

  
**YEAR**

2015
------

**LAND APPLICATION AREA MONITORING TOTAL NITROGEN LOADING RESULTS**

LAA Field	Gobel	MS 1	MS 2	MS 3	MS 5	MS 6	MS 11	MS 14	MS 15	MS 16	MS 18a	MS 18b	MS 20a	MS 20b	MS 21	MS 24a	MS 24b	MS 24c	MS 24d
Acres of LAA Irrigated																			
Total Nitrogen Loading from Wastewater (lbs/ac/month)																			
Total Nitrogen Loading Rate from Settling Pond Solids (lbs/ac/month)																			
Total Nitrogen Loading Rate from Cooling Pond Solids (lbs/ac/month)																			
Total Nitrogen Loading Rate from Residual Solids (lbs/ac/month)																			
Total Nitrogen Loading Rate from Cattle/ Manure (lbs/ac/month)																			
Total Nitrogen Loading Rate from Commercial Fertilizers (lbs/ac/month)																			
Cumulative Annual Total Nitrogen Value (lbs/ac/year)																			
Annual Crop Demand (lbs/ac/year)																			

# **Attachment F**

**DISCHARGER: Morning Star Packing Company, LP and Fred Gobel**  
**FACILITY: Morning Star Tomato Packing Plant**  
**COUNTY: Colusa**  
**WDRs Order: R5-2013-0144**

**MONTHLY MONITORING REPORT : Facility Not Processing, Land Application Monitoring N/A**

<b>MONTH</b>	April
<b>YEAR</b>	2015

**LAND APPLICATION AREA WASTEWATER INSPECTION MONITORING**

<b>Field No.</b>		<b>Technician</b>	
<b>Date</b>		<b>Weather</b>	

- 1. Any evidence of erosion: yes/no \_\_\_\_\_
- 2. Berm Condition: \_\_\_\_\_
- 3. Standpipe and flow control valve condition \_\_\_\_\_
- 4. Are the valves being used properly: yes/no \_\_\_\_\_
- 5. Is there any soil saturation: yes/no \_\_\_\_\_
- 6. Is there any ponding: yes/no \_\_\_\_\_
- 7. Is there any potential runoff to offsite areas: yes/no \_\_\_\_\_
- 8. Is there any potential and actual discharge to surface water: yes/no \_\_\_\_\_
- 9. Are there any accumulation of organic solids at soil surface: yes/no \_\_\_\_\_
- 10. Is there any soil clogging: yes/no \_\_\_\_\_
- 11. Are there any odors that have the potential to be objectionable at or beyond the property boundary: yes/no \_\_\_\_\_
- 12. Are there any insects: yes/no \_\_\_\_\_
- 13. Temperature and wind direction/strength \_\_\_\_\_
- 14. Other observations \_\_\_\_\_

**At least once per week when wastewater is being applied to the land application areas, the application areas in use shall be inspected to identify any equipment malfunction or other circumstance that might allow wastewater or irrigation runoff to leave each LAA and/or create conditions that violate the Waste Discharge Requirements. A log of these inspections shall be kept at the facility and summarized for submittal with the monthly monitoring reports.**

**In accordance with Section A.5 of the Monitoring Report, please attach a current site plan depicting the irrigation checks within each LAA field that will be used during the calendar year, including all water conveyance ditches and internal berms that divide each LAA (where applicable).**

# **Attachment G**

**DISCHARGER:** Morning Star Packing Company, LP and Fred Gobel  
**FACILITY:** Morning Star Tomato Packing Plant  
**COUNTY:** Colusa  
**WDRs Order** R5-2013-0144

**MONTHLY MONITORING REPORT**

<b>MONTH</b>	April
<b>YEAR</b>	2015

**RESIDUAL SOLIDS MONITORING** : Facility Not Processing, Solids Monitoring N/A

<b>Date</b>	<b>Type of Solids Generated</b>	<b>Volume of Solids Generated (tons)<sup>1</sup></b>	<b>Volume of Solids Disposed of Offsite (tons)</b>	<b>Offsite Solids Disposal Location<sup>2</sup></b>	<b>Volume of Solids Disposed of Onsite (tons)</b>	<b>Onsite Solids Disposal Location<sup>3</sup></b>

<sup>1</sup>Volume of Solids Generated. Solids may include pomace, seeds, stems, diatomaceous earth, screenings, pond solids, and sump solids, or other material.

<sup>2</sup>Volume Disposed of Off-site. Describe the disposal method (e.g. animal feed, land application, off-site composting, landfill, etc.) and the name of the hauling company.

<sup>3</sup>Volume Disposed of On-site; location of on-site disposal (e.g. land application area field); method of application, spreading, and incorporation; application rate (tons/acre), and results from weekly grab sample analysis for total nitrogen.

# **Attachment H**

DISCHARGE Morning Star Packing Company, LP and Fred Gobel  
 FACILITY: Morning Star Tomato Packing Plant  
 COUNTY: Colusa  
 WDRs Order R5-2013-0144

**MONTHLY MONITORING REPORT : No water in pond**

MONTH	April
YEAR	2015

**FIELD INSTRUMENT CALIBRATION LOG**

Monitoring Week	Date	Time	Lower Standard pH Buffer	Lower Standard Stabilized pH	Lower pH Standard Calibrated pH	Upper Standard pH Buffer	Upper Standard Stabilized pH	Upper Standard Calibrated pH	DO Initial Reading	Electrolyte Solution Added	DO Reading after Calibration	Technican's Initials
Week 1												
Week 2												
Week 3												
Week 4												
Week 5												

If either calibrated pH value is more than 0.2 higher or lower than its corresponding pH buffer value, recalibrate the meter before using it in the field.



# INSTRUMENT CALIBRATION REPORT

Aqua Sierra Controls, Inc.  
 1650 Industrial Drive  
 Auburn, CA 95603  
 Phone (800) 649-4287  
 Fax (530) 823-3475  
 service@aquasierra.com  
 www.aquasierra.com

Attn: JAMES BRISCO  
 MORNING STAR PACKING COMPANY  
 2211 OLD HIGHWAY 99  
 WILLIAMS, CA 95987

Instrument ID 01  
 Description FLOW METER

Serial Number AIJ001295  
 Model Number U SONIC R

Calibrated 5/30/2014  
 Scheduled 5/30/2015  
 Calibration ID 21526  
 Certificate # 01  
 Equipment ID

Department  
 Manufacturer DREXEL BROOK  
 Calibration Type INITIAL  
 Location SETTLING POND  
 Building OUTSIDE

<u>Calibration Specifications</u>							
Stated Accy		Pct of Reading					
<u>In Val</u>	<u>In Type</u>	<u>Out Val</u>	<u>Out Type</u>	<u>Fnd As</u>	<u>Error %</u>	<u>Lft As</u>	<u>Error %</u>
0.00	FEET H2O	0.00	GPM	0.00	0.00%	0.00	0.00%
0.20	FEET H2O	334.20	GPM	330.00	-1.26%	330.00	-1.26%
0.54	FEET H2O	1483.00	GPM	1,483.00	0.00%	1,483.00	0.00%
0.71	FEET H2O	2235.00	GPM	2,275.00	1.79%	2,275.00	1.79%
0.87	FEET H2O	3032.00	GPM	3,068.00	1.19%	3,068.00	1.19%

<u>Test Instruments Used During the Calibration</u>				
<u>Test Instrument ID</u>	<u>Description</u>	<u>Manufacturer</u>	<u>Model Number</u>	<u>Serial Number</u>
101	ULTRASONIC TEST STAND	ASC	1076-10	ASC-04-KEN

Notes about this calibration

2.5' RECTANGULAR WEIR  
 ZERO DISTANCE = 2.74'  
 VERIFIED LEVEL READING AT WEIR

Calibration Result Calibration Successful  
 Who Calibrated KEN LANE



# INSTRUMENT CALIBRATION REPORT

Aqua Sierra Controls, Inc.  
 1650 Industrial Drive  
 Auburn, CA 95603  
 Phone (800) 649-4287  
 Fax (530) 823-3475  
 service@aquasierra.com  
 www.aquasierra.com

**Attn: JAMES BRISCO**  
**MORNING STAR PACKING COMPANY**  
 2211 OLD HIGHWAY 99  
 WILLIAMS, CA 95987

**Instrument ID** 02  
**Description** FLOW METER

**Serial Number** A1J000210  
**Model Number** U SONIC R

**Calibrated** 5/30/2014  
**Scheduled** 5/30/2015  
**Calibration ID** 21527  
**Certificate #** 02  
**Equipment ID**

**Department**  
**Manufacturer** DREXEL BROOK  
**Calibration Type** INITIAL  
**Location** COOLING POND  
**Building** OUTSIDE

<u>Calibration Specifications</u>							
Stated Accy		Pct of Reading					
<u>In Val</u>	<u>In Type</u>	<u>Out Val</u>	<u>Out Type</u>	<u>End As</u>	<u>Error %</u>	<u>Lft As</u>	<u>Error %</u>
0.00	FEET H2O	0.00	GPM	0.00	0.00%	0.00	0.00%
0.22	FEET H2O	301.70	GPM	299.00	-0.89%	299.00	-0.89%
0.41	FEET H2O	752.80	GPM	749.00	-0.50%	749.00	-0.50%
0.55	FEET H2O	1153.00	GPM	1,174.00	1.82%	1,174.00	1.82%
0.67	FEET H2O	1530.00	GPM	1,542.00	0.78%	1,542.00	0.78%

<u>Test Instruments Used During the Calibration</u>				
<u>Test Instrument ID</u>	<u>Description</u>	<u>Manufacturer</u>	<u>Model Number</u>	<u>Serial Number</u>
101	ULTRASONIC TEST STAND	ASC	1076-10	ASC-04-KEN

**Notes about this calibration**  
 2' RECTANGULAR WEIR WITH END CONTRACTIONS  
 ZERO DISTANCE = 32.6" OR 2.72'  
 CHANNEL #2

**Calibration Result** Calibration Successful  
**Who Calibrated** KEN LANE



# INSTRUMENT CALIBRATION REPORT

Aqua Sierra Controls, Inc.  
 1650 Industrial Drive  
 Auburn, CA 95603  
 Phone (800) 649-4287  
 Fax (530) 823-3475  
 service@aquasierra.com  
 www.aquasierra.com

**Attn:** JAMES BRISCO  
**MORNING STAR PACKING COMPANY**  
 2211 OLD HIGHWAY 99  
 WILLIAMS, CA 95987

**Instrument ID** 03  
**Description** FLOW METER

**Serial Number** A1J000210  
**Model Number** U SONIC R

**Calibrated** 5/30/2014  
**Scheduled** 5/30/2015  
**Calibration ID** 21524  
**Certificate #** 03  
**Equipment ID**

**Department**  
**Manufacturer** DREXEL BROOK  
**Calibration Type** INITIAL  
**Location** MAIN DITCH  
**Building** OUTSIDE

<u>Calibration Specifications</u>							
Stated Accy		Pct of Reading					
<u>In Val</u>	<u>In Type</u>	<u>Out Val</u>	<u>Out Type</u>	<u>Fnd As</u>	<u>Error %</u>	<u>Lft As</u>	<u>Error %</u>
0.00	FEET H2O	0.00	GPM	0.00	0.00%	0.00	0.00%
0.20	FEET H2O	334.20	GPM	340.00	1.74%	340.00	1.74%
0.54	FEET H2O	1483.00	GPM	1,476.00	-0.47%	1,476.00	-0.47%
0.71	FEET H2O	2235.00	GPM	2,228.00	-0.31%	2,228.00	-0.31%
0.87	FEET H2O	3032.00	GPM	3,048.00	0.53%	3,048.00	0.53%

**Test Instruments Used During the Calibration**

<u>Test Instrument ID</u>	<u>Description</u>	<u>Manufacturer</u>	<u>Model Number</u>	<u>Serial Number</u>
101	ULTRASONIC TEST STAND	ASC	1076-10	ASC-04-KEN

**Notes about this calibration**

2.5' RECTANGULAR WEIR  
 CHANNEL #1  
 ZERO DISTANCE MEASURED AT 3.13'  
 VERIFIED LEVEL READING AT WEIR

**Calibration Result** Calibration Successful  
**Who Calibrated** KEN LANE
