Exhibit 5

Prosecution Team Evidence List Exhibits for:

Rocklin Crossings

DIGITALSKY
AERIAL IMAGING
2378 Maritime Dr., Suite 200, Elk Grove, CA 95758
Phone (916) 691-6090 Email todd@digitalsky.us
November 26th, 2012

_D1W0103

12/3/12

_MG_1535

12/3/12

_MG_1552

12/3/12

_MG_1556

12/3/12

SD DEACON
GENERAL CONTRACTOR

ROCKLIN CROSSINGS

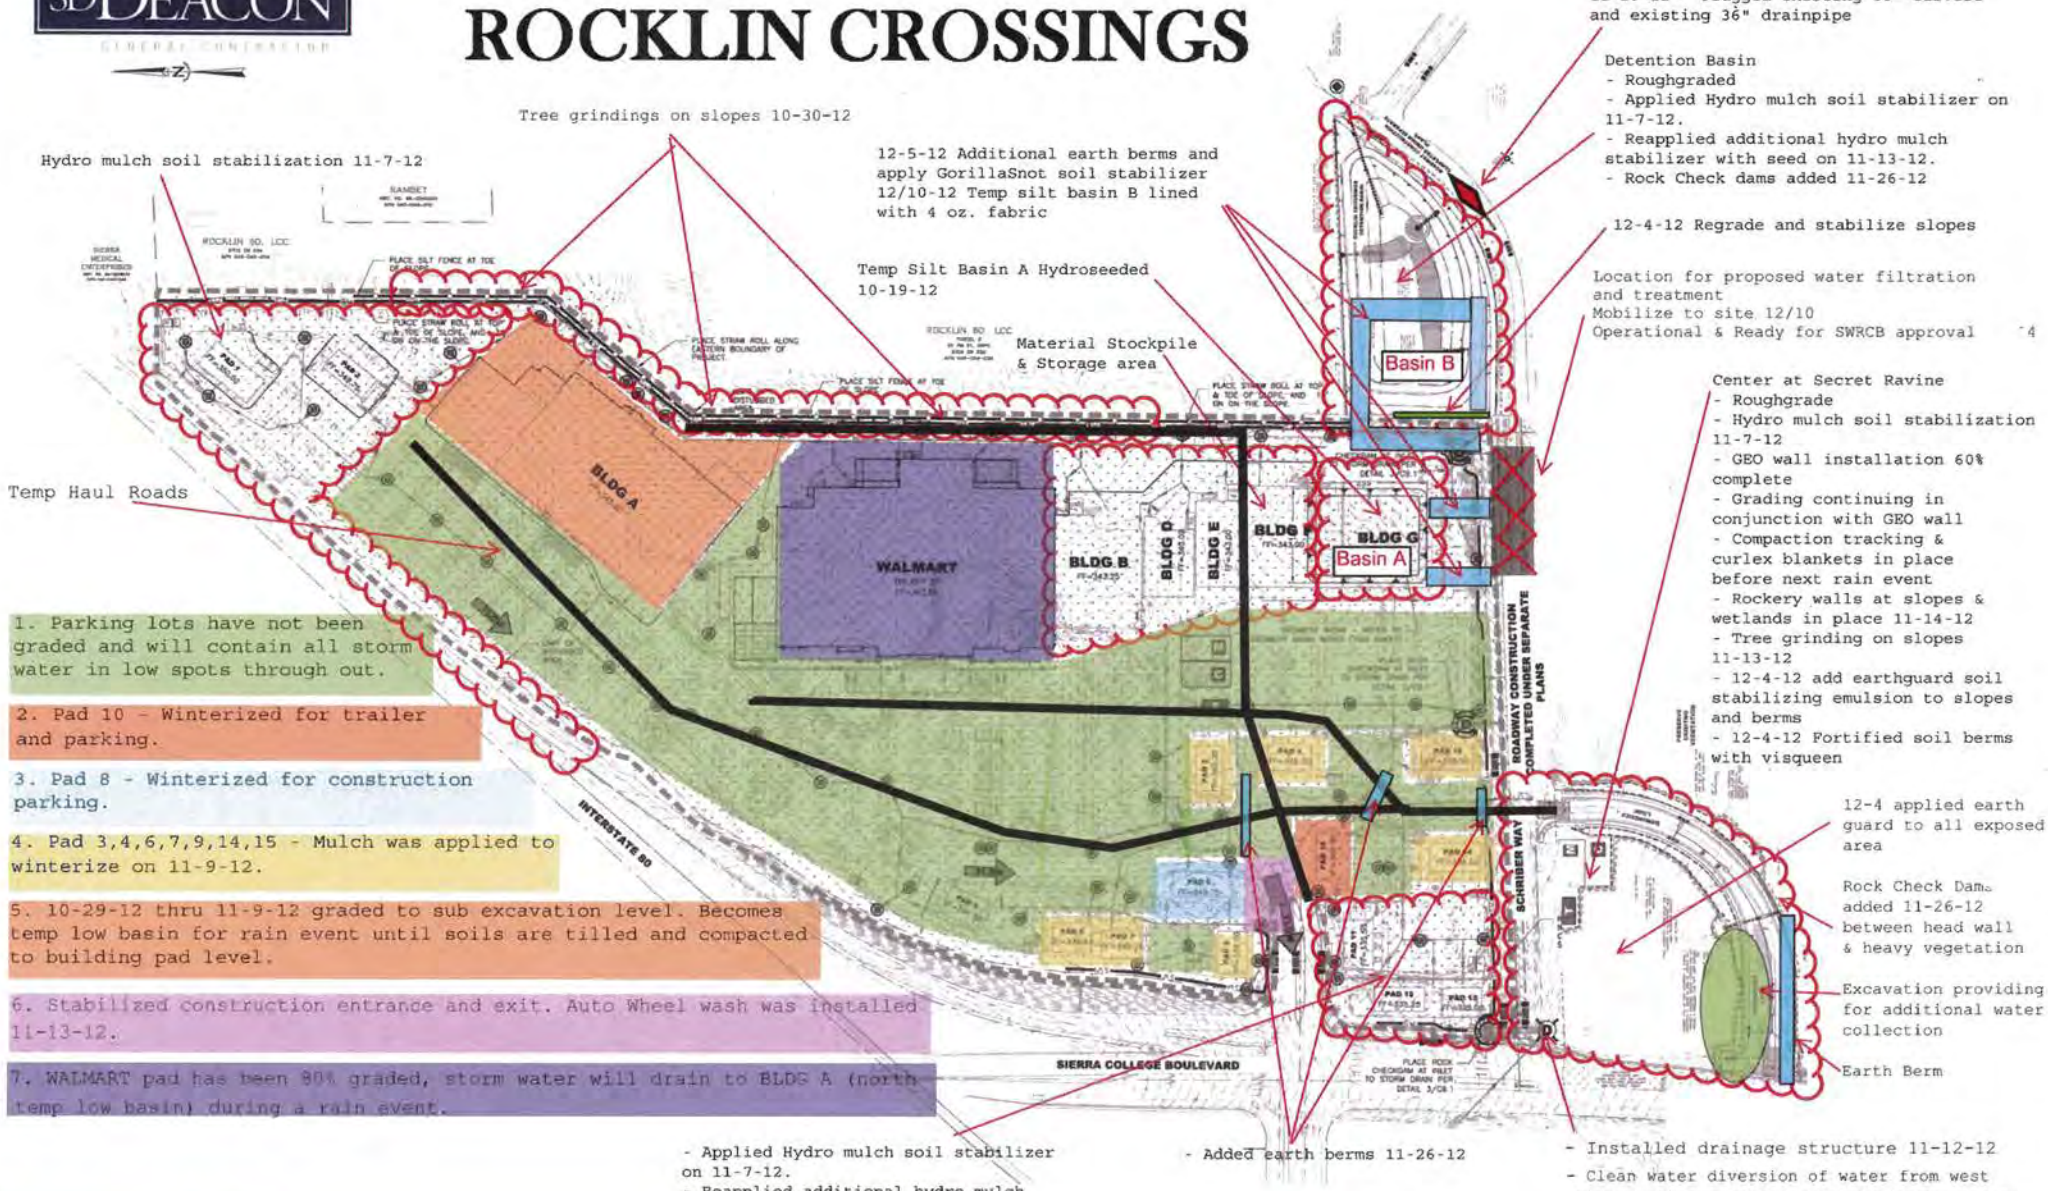

Date Revised - 12-7-12

DRAFT

Rocklin Crossings phased grading plan

1. Contract with water treatment company ATS Environmental Inc to treat, filter and discharge water with an approved ATS plan
2. Build out of additional emergency temporary silt basin (labeled Basin B) Dec 6-7
3. Line basin B with 4oz non-woven fabric, bottom sides and back slopes Dec 10
4. ATS equipment begins mobilization Dec 10 expected to be ready for operations by Dec 14 upon approval by SWRCB of ATS plan
5. Pump water from Center @ Secret Ravine (C@SR) into Basin B Dec 10-11
6. Pump water from various low lying areas throughout the site into Basin B Dec 11-14
7. Re-apply soil stabilizers to SW village area and to C@SR Dec 11 prior to forecasted rain event of Dec 12
8. Establish all weather access road into and across site to Wal-Mart (WM) staging area Dec 13-14
9. Install base rock to staging area at majors B-E pads Dec 14
10. Cut to subex grades at SW village area and fill to final grades in C@SR = 2 shifts
11. Apply soil stabilizers and plan BMP's to C@SR and fence off all access = 1 shift
12. Finish grade and certify building pads 3, 4, 5, 6, 7, 9, 14 and 15 = 1 shift
13. Apply final BMP's to building = pads 3, 4, 5, 6, 7, 9, 14 and 15 = 1 shift
14. Remove rock from WM sub ex to SW village deeper fill areas = 4 shifts
15. Top off SW village including pads 11, 12 and 13 =3 shifts
16. Apply final BMP's to SW village and building pads = 1 shift
17. Complete WM pad backfill and final grading = 10 shifts
18. Apply final BMP's to WM pad = 1 shift
19. Install all weather access roads around WM pad = 3 shifts
20. Basin A and B will remain in place as water retention and settling basins for water treatment through March 2013

12/11/2012 4:11 PM – Rec'd on 12/12/12 @ 1130 meeting

Rain Gauge Log Sheet

Construction Site Name: Rocklin Crossing JOB # 992

WDID #:

Date (mm/dd/yy)	Time (24-hr)	Initials	Rainfall Depth (Inches)	Notes:
NOV 1.12	9AM	BH	1/2	RAIN FALL From 830pm 9AM measured 10/31 - 11/1
11/8/12	5:30 AM	D	1/4	RAIN 11:30pm - 5:30AM 11/8 - 11/9
11/29/12	8:00A.M -7.00AM	D	3/4"	RAIN FALL From 8:00A.M - 7:AM 11/28 - 11/29
12/2/12		~~BH~~	6 1/4"	RAIN FALL From 5pm - 7AM 11/30 12/2
12/5/12		D	7/8"	RAW FALL From 11:00AM 4:00P.M. 12/5 12/5

7" rainfall for 11/28 → 12/2/12 storm event.

Rocklin Crossings phased grading plan

1. Contract with water treatment company ATS Environmental Inc to treat, filter and discharge water with an approved ATS plan
2. Build out of additional emergency temporary silt basin (labeled Basin B) Dec 6-7
3. Line basin B with 4oz non-woven fabric, bottom sides and back slopes Dec 10
4. ATS equipment begins mobilization Dec 10 expected to be ready for operations by Dec 14 upon approval by SWRCB of ATS plan
5. Pump water from Center @ Secret Ravine (C@SR) into Basin B Dec 10-11
6. Pump water from various low lying areas throughout the site into Basin B Dec 11-14
7. Re-apply soil stabilizers to SW village area and to C@SR Dec 11 prior to forecasted rain event of Dec 12
8. Establish all weather access road into and across site to Wal-Mart (WM) staging area Dec 13-14
9. Install base rock to staging area at majors B-E pads Dec 14
10. Cut to subex grades at SW village area and fill to final grades in C@SR = 2 shifts
11. Apply soil stabilizers and plan BMP's to C@SR and fence off all access = 1 shift
12. Finish grade and certify building pads 3, 4, 5, 6, 7, 9, 14 and 15 = 1 shift
13. Apply final BMP's to building = pads 3, 4, 5, 6, 7, 9, 14 and 15 = 1 shift
14. Remove rock from WM sub ex to SW village deeper fill areas = 4 shifts
15. Top off SW village including pads 11, 12 and 13 =3 shifts
16. Apply final BMP's to SW village and building pads = 1 shift
17. Complete WM pad backfill and final grading = 10 shifts
18. Apply final BMP's to WM pad = 1 shift
19. Install all weather access roads around WM pad = 3 shifts
20. Basin A and B will remain in place as water retention and settling basins for water treatment through March 2013

Basin B

PAD 1 6,500 SF

PAD 2 5,000 SF

MAJOR A (HOME DEPOT) 105,920 SF GARDEN CENTER 24,000 SF

WAL*MART #3587-02
C-180-SGL-NO
WITH INDOOR GARDEN CENTER & CANOPIES
185,667 SF
OUTDOOR GARDEN CENTER
8,878 SF
5454 CROSSINGS DRIVE

MAJOR B 35,000 SF

MAJOR D 13,500 SF

MAJOR E 15,200 SF

Basin A

MA 35,500 SF

35,500 SF

PAD 3 5,500 SF

PAD 4 4,800 SF

PAD 15 5,000 SF

PAD 5 5,000 SF

PAD 8 6,000 SF

PAD 10 4,750 SF

PAD 14 6,000 SF

PAD 6 4,800 SF

PAD 7 4,800 SF

PAD 9 5,100 SF

PAD 11 5,000 SF

PAD 12 5,000 SF

PAD 13 4,800 SF

CENTER @ SECRET RAVINE

ROCKLIN CROSSINGS

I 80 AND SIERRA COLLEGE BLVD
CITY OF ROCKLIN, CA

DATE:
