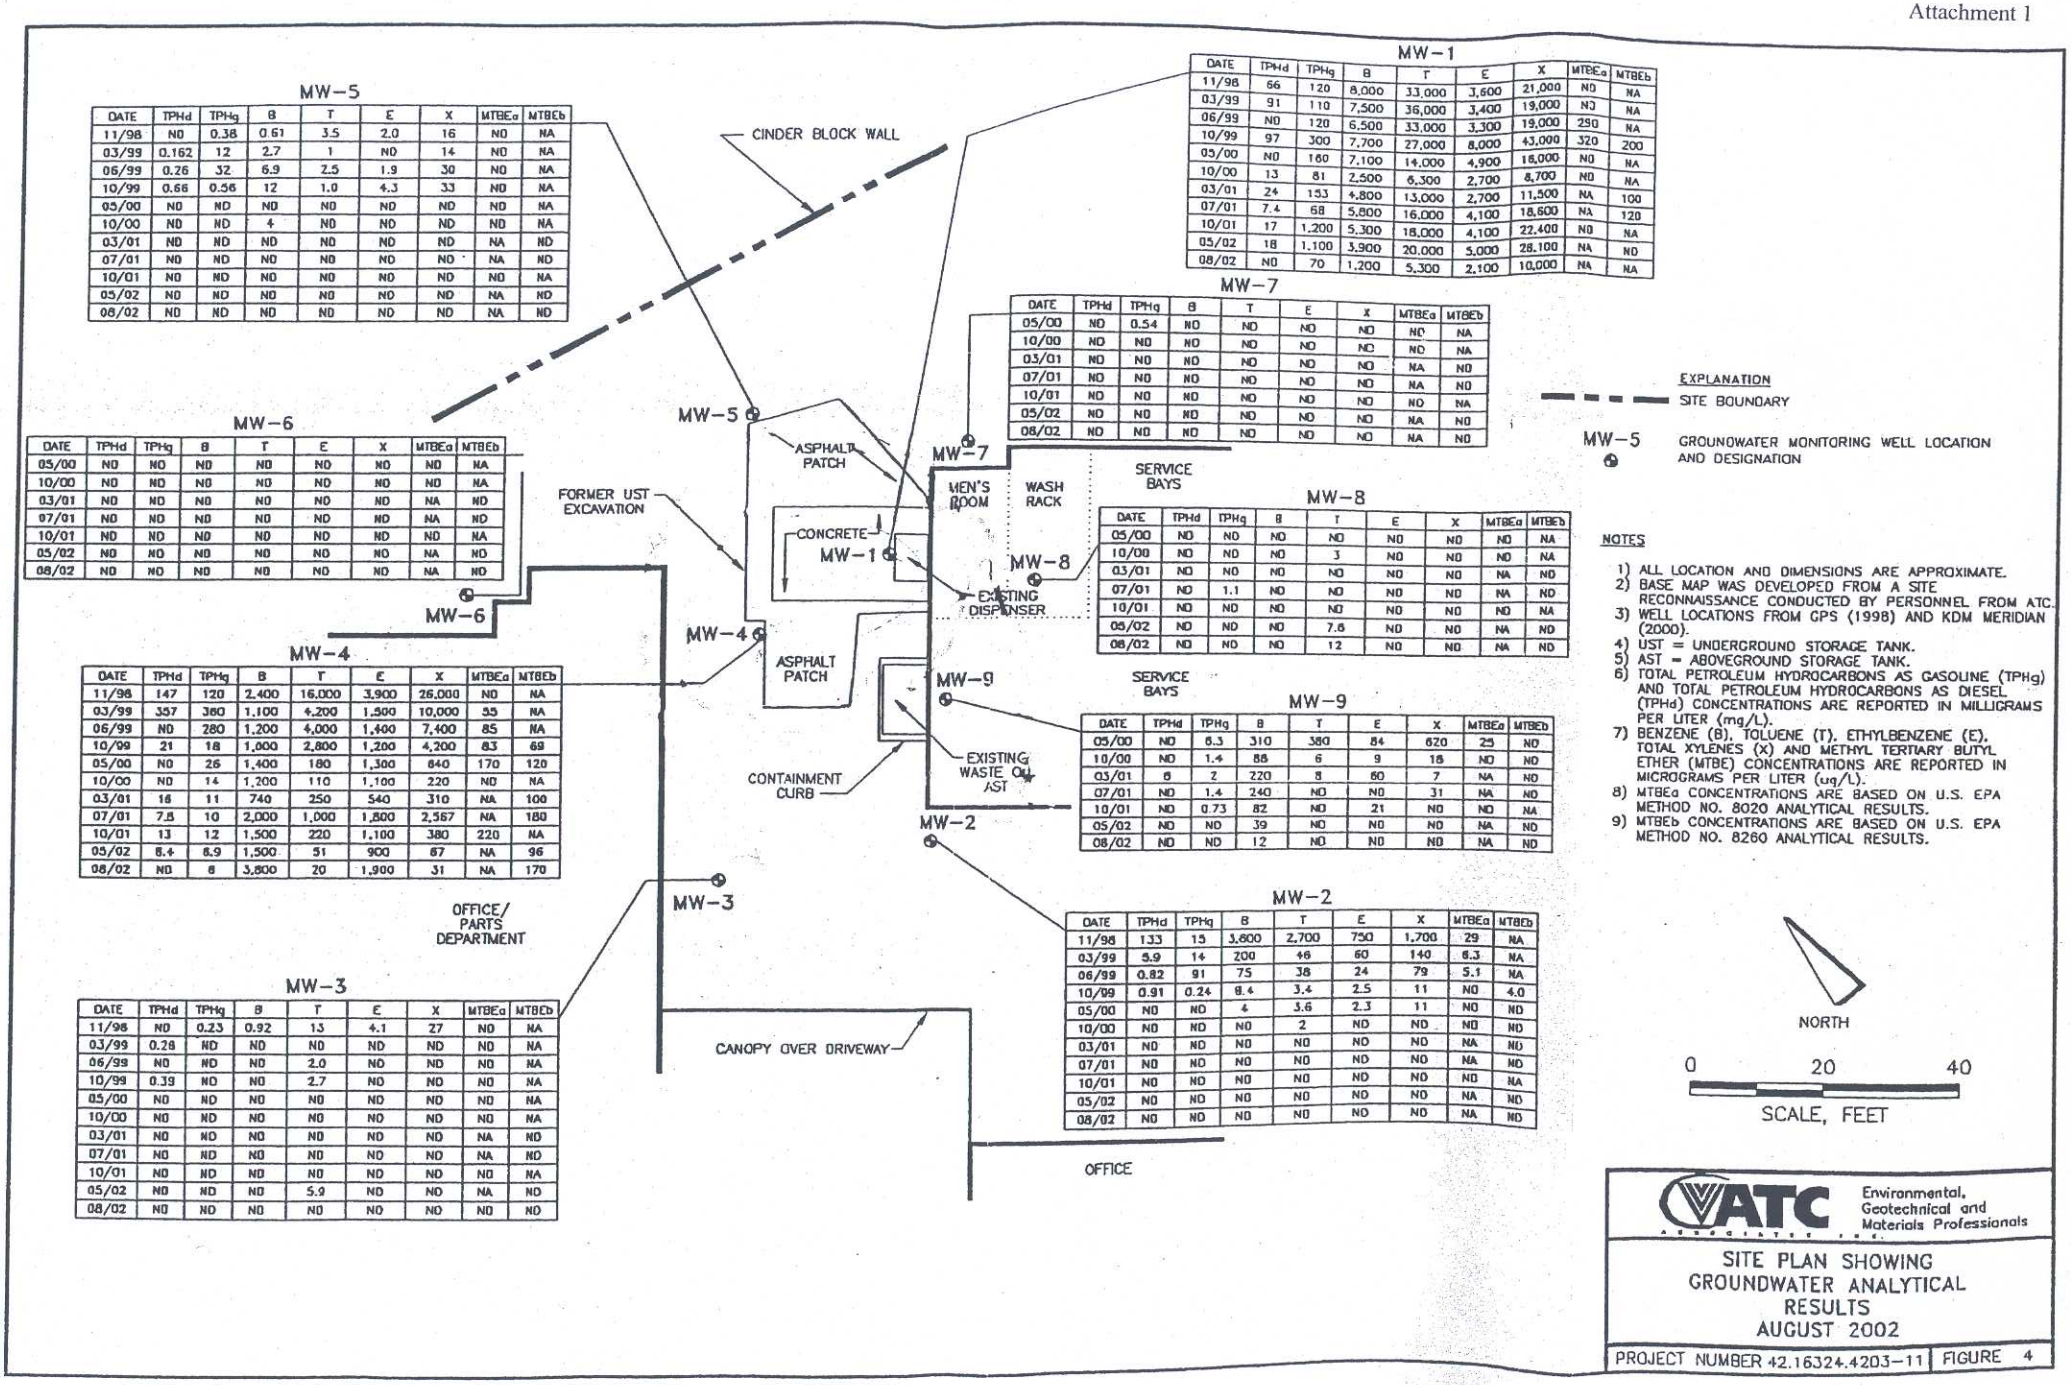

MW-5

DATE	TPHd	TPHg	B	T	E	X	MTBEa	MTBEb
11/98	ND	0.38	0.61	3.5	2.0	16	ND	NA
03/99	0.162	12	2.7	1	ND	14	ND	NA
06/99	0.26	32	6.9	2.5	1.9	30	ND	NA
10/99	0.66	0.56	12	1.0	4.3	33	ND	NA
05/00	ND	ND	ND	ND	ND	ND	ND	NA
10/00	ND	ND	4	ND	ND	ND	ND	NA
03/01	ND	ND	ND	ND	ND	ND	NA	ND
07/01	ND	ND	ND	ND	ND	ND	NA	ND
10/01	ND	ND	ND	ND	ND	ND	ND	NA
05/02	ND	ND	ND	ND	ND	ND	NA	ND
08/02	ND	ND	ND	ND	ND	ND	NA	ND

MW-1

DATE	TPHd	TPHg	B	T	E	X	MTBEa	MTBEb
11/98	66	120	8,000	33,000	3,600	21,000	ND	NA
03/99	91	110	7,500	36,000	3,400	19,000	ND	NA
06/99	ND	120	6,500	33,000	3,300	19,000	290	NA
10/99	97	300	7,700	27,000	8,000	43,000	320	200
05/00	ND	160	7,100	14,000	4,900	16,000	ND	NA
10/00	13	81	2,500	6,300	2,700	8,700	ND	NA
03/01	24	153	4,800	13,000	2,700	11,500	NA	100
07/01	7.4	68	5,800	16,000	4,100	18,600	NA	120
10/01	17	1,200	5,300	18,000	4,100	22,400	ND	NA
05/02	18	1,100	3,900	20,000	5,000	28,100	NA	ND
08/02	ND	70	1,200	5,300	2,100	10,000	NA	NA

MW-7

DATE	TPHd	TPHg	B	T	E	X	MTBEa	MTBEb
05/00	ND	0.54	ND	ND	ND	ND	ND	NA
10/00	ND	ND	ND	ND	ND	ND	ND	NA
03/01	ND	ND	ND	ND	ND	ND	NA	ND
07/01	ND	ND	ND	ND	ND	ND	NA	ND
10/01	ND	ND	ND	ND	ND	ND	ND	NA
05/02	ND	ND	ND	ND	ND	ND	NA	ND
08/02	ND	ND	ND	ND	ND	ND	NA	ND

MW-6

DATE	TPHd	TPHg	B	T	E	X	MTBEa	MTBEb
05/00	ND	ND	ND	ND	ND	ND	ND	NA
10/00	ND	ND	ND	ND	ND	ND	ND	NA
03/01	ND	ND	ND	ND	ND	ND	NA	ND
07/01	ND	ND	ND	ND	ND	ND	NA	ND
10/01	ND	ND	ND	ND	ND	ND	ND	NA
05/02	ND	ND	ND	ND	ND	ND	NA	ND
08/02	ND	ND	ND	ND	ND	ND	NA	ND

MW-8

DATE	TPHd	TPHg	B	T	E	X	MTBEa	MTBEb
05/00	ND	ND	ND	ND	ND	ND	ND	NA
10/00	ND	ND	ND	3	ND	ND	ND	NA
03/01	ND	ND	ND	ND	ND	ND	NA	ND
07/01	ND	1.1	ND	ND	ND	ND	NA	ND
10/01	ND	ND	ND	ND	ND	ND	ND	NA
05/02	ND	ND	ND	7.6	ND	ND	NA	ND
08/02	ND	ND	ND	12	ND	ND	NA	ND

MW-4

DATE	TPHd	TPHg	B	T	E	X	MTBEa	MTBEb
11/98	147	120	2,400	16,000	3,900	26,000	ND	NA
03/99	357	360	1,100	4,200	1,500	10,000	55	NA
06/99	ND	280	1,200	4,000	1,400	7,400	85	NA
10/99	21	18	1,000	2,800	1,200	4,200	83	69
05/00	ND	26	1,400	180	1,300	640	170	120
10/00	ND	14	1,200	110	1,100	220	ND	NA
03/01	16	11	740	250	540	310	NA	100
07/01	7.8	10	2,000	1,000	1,800	2,567	NA	180
10/01	13	12	1,500	220	1,100	380	220	NA
05/02	8.4	8.9	1,500	51	900	67	NA	96
08/02	ND	6	3,800	20	1,900	31	NA	170

MW-9

DATE	TPHd	TPHg	B	T	E	X	MTBEa	MTBEb
05/00	ND	6.3	310	380	84	620	25	ND
10/00	ND	1.4	88	6	9	18	ND	ND
03/01	6	2	220	8	60	7	NA	ND
07/01	ND	1.4	240	ND	ND	31	NA	ND
10/01	ND	0.73	82	ND	21	ND	ND	NA
05/02	ND	ND	39	ND	ND	ND	NA	ND
08/02	ND	ND	12	ND	ND	ND	NA	ND

MW-3

DATE	TPHd	TPHg	B	T	E	X	MTBEa	MTBEb
11/98	ND	0.23	0.92	13	4.1	27	ND	NA
03/99	0.28	ND	ND	ND	ND	ND	ND	NA
06/99	ND	ND	ND	2.0	ND	ND	ND	NA
10/99	0.39	ND	ND	2.7	ND	ND	ND	NA
05/00	ND	ND	ND	ND	ND	ND	ND	NA
10/00	ND	ND	ND	ND	ND	ND	ND	NA
03/01	ND	ND	ND	ND	ND	ND	NA	ND
07/01	ND	ND	ND	ND	ND	ND	NA	ND
10/01	ND	ND	ND	ND	ND	ND	ND	NA
05/02	ND	ND	ND	5.9	ND	ND	NA	ND
08/02	ND	ND	ND	ND	ND	ND	ND	ND

MW-2

DATE	TPHd	TPHg	B	T	E	X	MTBEa	MTBEb
11/98	133	15	3,600	2,700	750	1,700	29	NA
03/99	5.9	14	200	46	60	140	6.3	NA
06/99	0.82	91	75	38	24	79	5.1	NA
10/99	0.91	0.24	8.4	3.4	2.5	11	ND	4.0
05/00	ND	ND	4	3.6	2.3	11	ND	ND
10/00	ND	ND	ND	2	ND	ND	ND	ND
03/01	ND	ND	ND	ND	ND	ND	NA	ND
07/01	ND	ND	ND	ND	ND	ND	NA	ND
10/01	ND	ND	ND	ND	ND	ND	ND	NA
05/02	ND	ND	ND	ND	ND	ND	NA	ND
08/02	ND	ND	ND	ND	ND	ND	NA	ND

NOTES

1) ALL LOCATION AND DIMENSIONS ARE APPROXIMATE.
2) BASE MAP WAS DEVELOPED FROM A SITE RECONNAISSANCE CONDUCTED BY PERSONNEL FROM ATC.
3) WELL LOCATIONS FROM GPS (1998) AND KDM MERIDIAN (2000).
4) UST = UNDERGROUND STORAGE TANK.
5) AST = ABOVEGROUND STORAGE TANK.
6) TOTAL PETROLEUM HYDROCARBONS AS GASOLINE (TPHg) AND TOTAL PETROLEUM HYDROCARBONS AS DIESEL (TPHd) CONCENTRATIONS ARE REPORTED IN MILLIGRAMS PER LITER (mg/L).
7) BENZENE (B), TOLUENE (T), ETHYLBENZENE (E), TOTAL XYLENES (X) AND METHYL TERTIARY BUTYL ETHER (MTBE) CONCENTRATIONS ARE REPORTED IN MICROGRAMS PER LITER (ug/L).
8) MTBEa CONCENTRATIONS ARE BASED ON U.S. EPA METHOD NO. 8020 ANALYTICAL RESULTS.
9) MTBEb CONCENTRATIONS ARE BASED ON U.S. EPA METHOD NO. 8260 ANALYTICAL RESULTS.

ATC ASSOCIATES INC. Environmental, Geotechnical and Materials Professionals

SITE PLAN SHOWING GROUNDWATER ANALYTICAL RESULTS AUGUST 2002

PROJECT NUMBER 42.16324.4203-11 | FIGURE 4
